

<Reference>

**Progress Status of the Ground Improvement/
Historical Data of Radioactive Density in
Groundwater at the East Side of Turbine Buildings**

July 18, 2014


Tokyo Electric Power Company




東京電力

TEPCO


Progress Status of Ground Improvement Construction between Units 1 and 2 (As of the Morning on July 18)

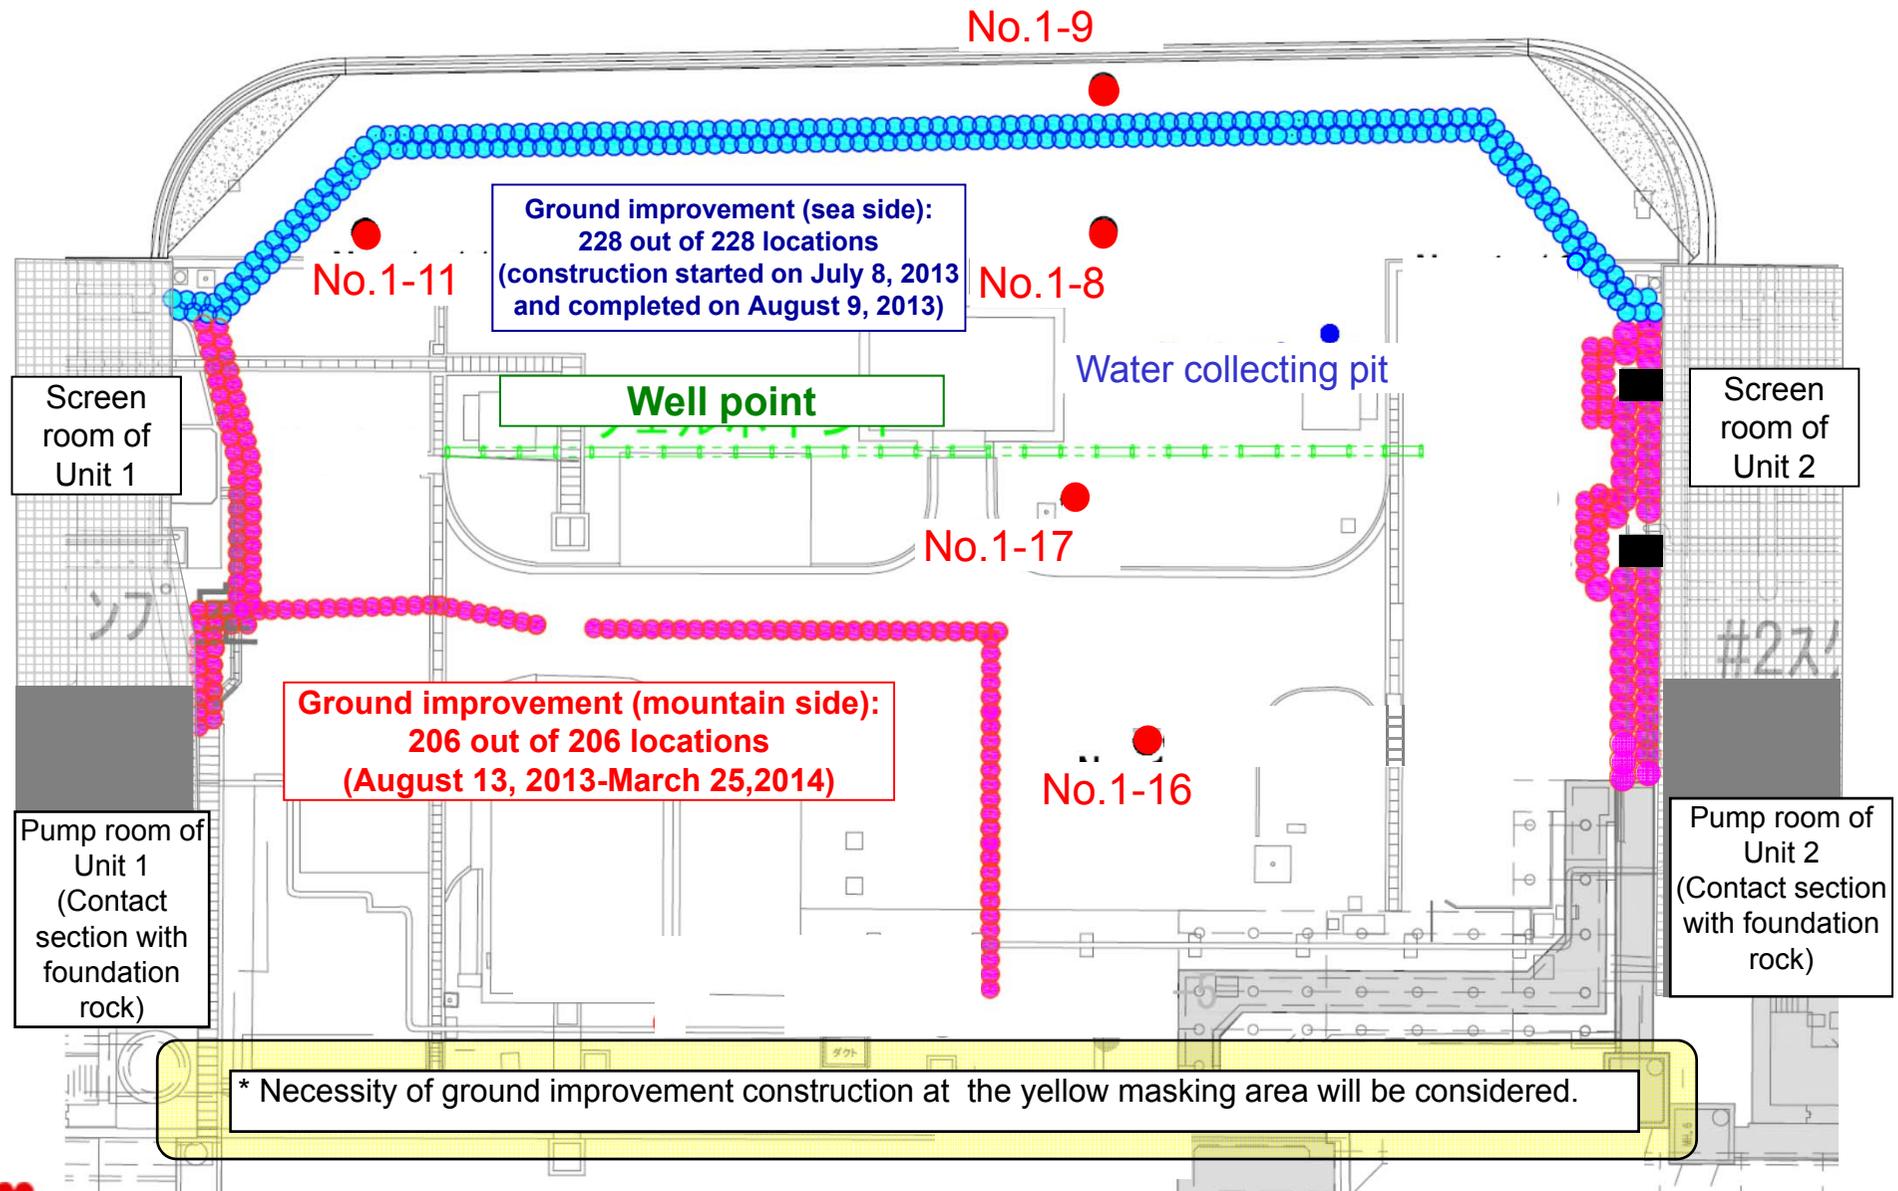

Progress Status of Ground Improvement Construction between Units 2 and 3 (As of the Morning on July 18)

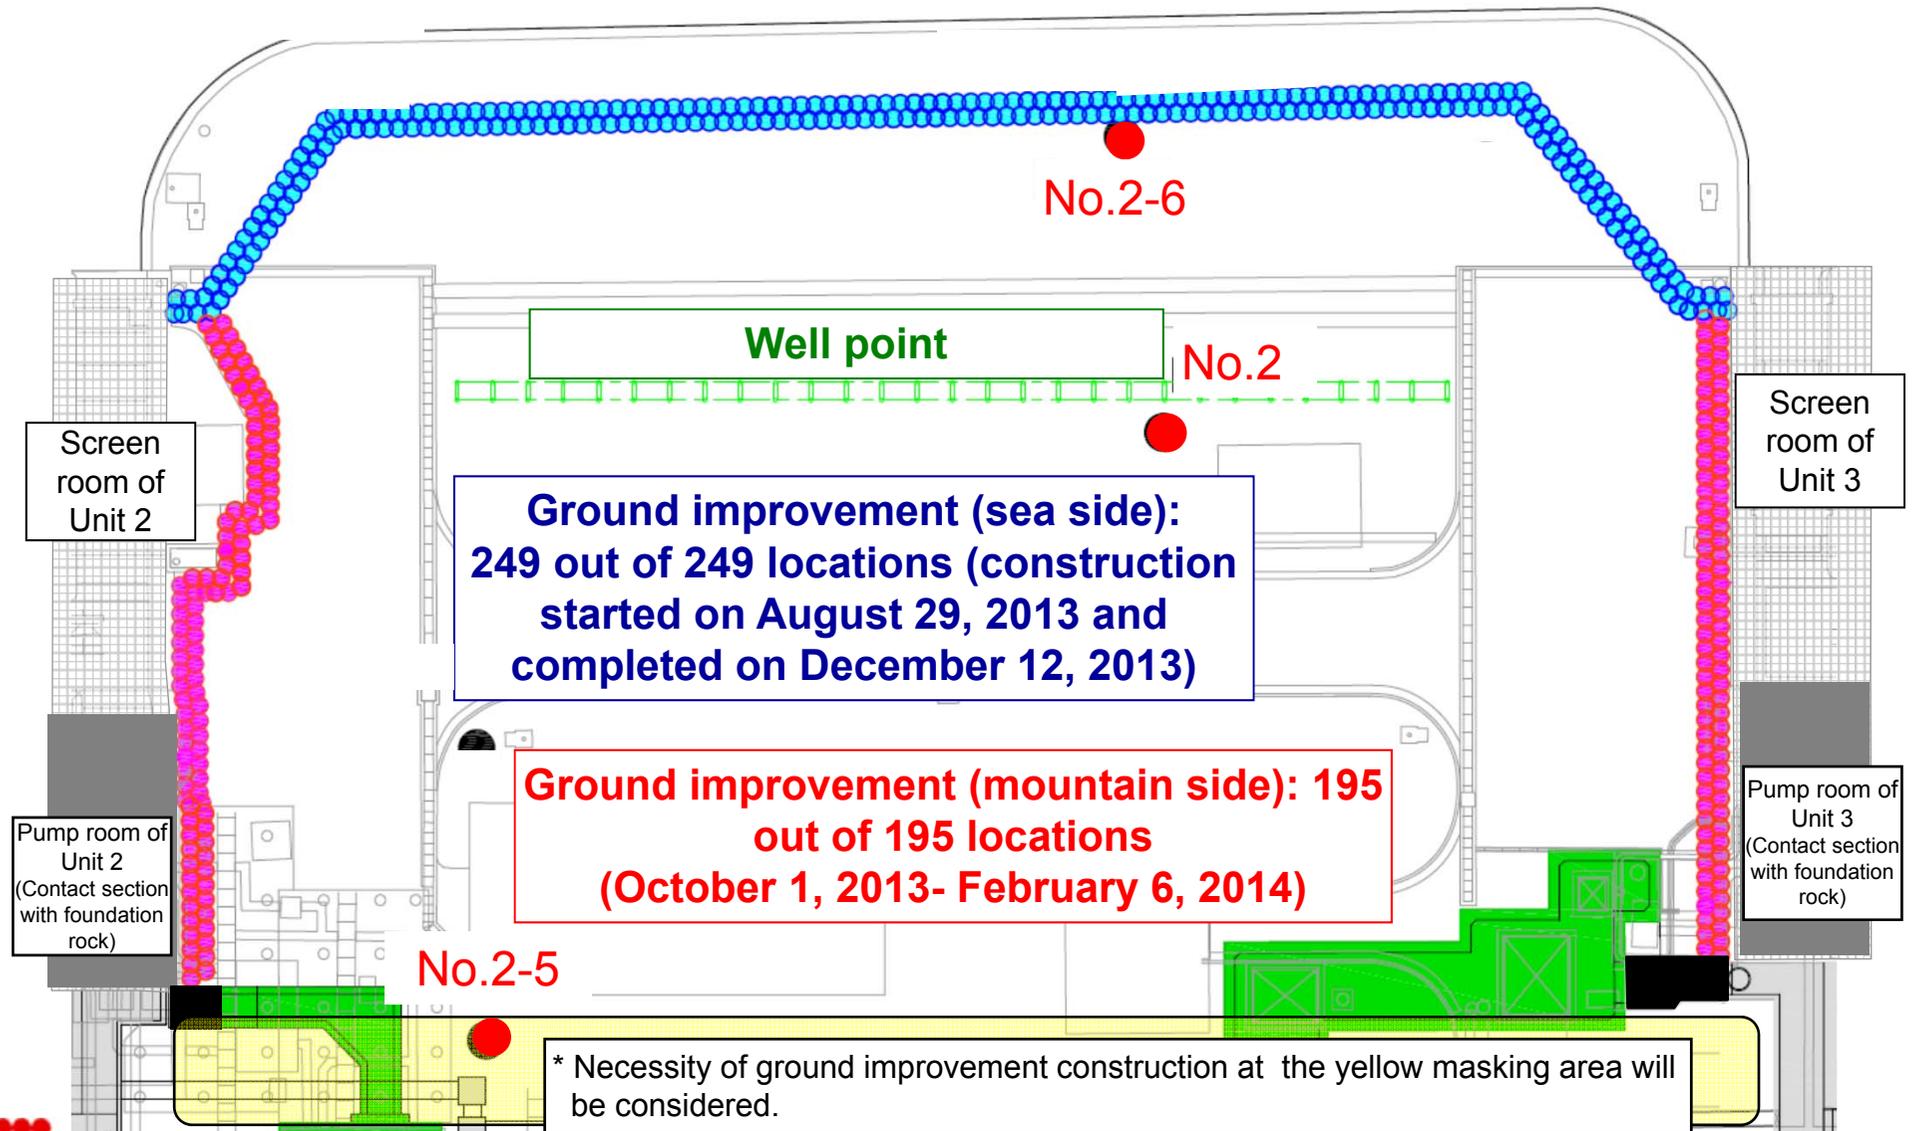

Progress Status of Ground Improvement Construction between Units 3 and 4 (As of the Morning on July 18)

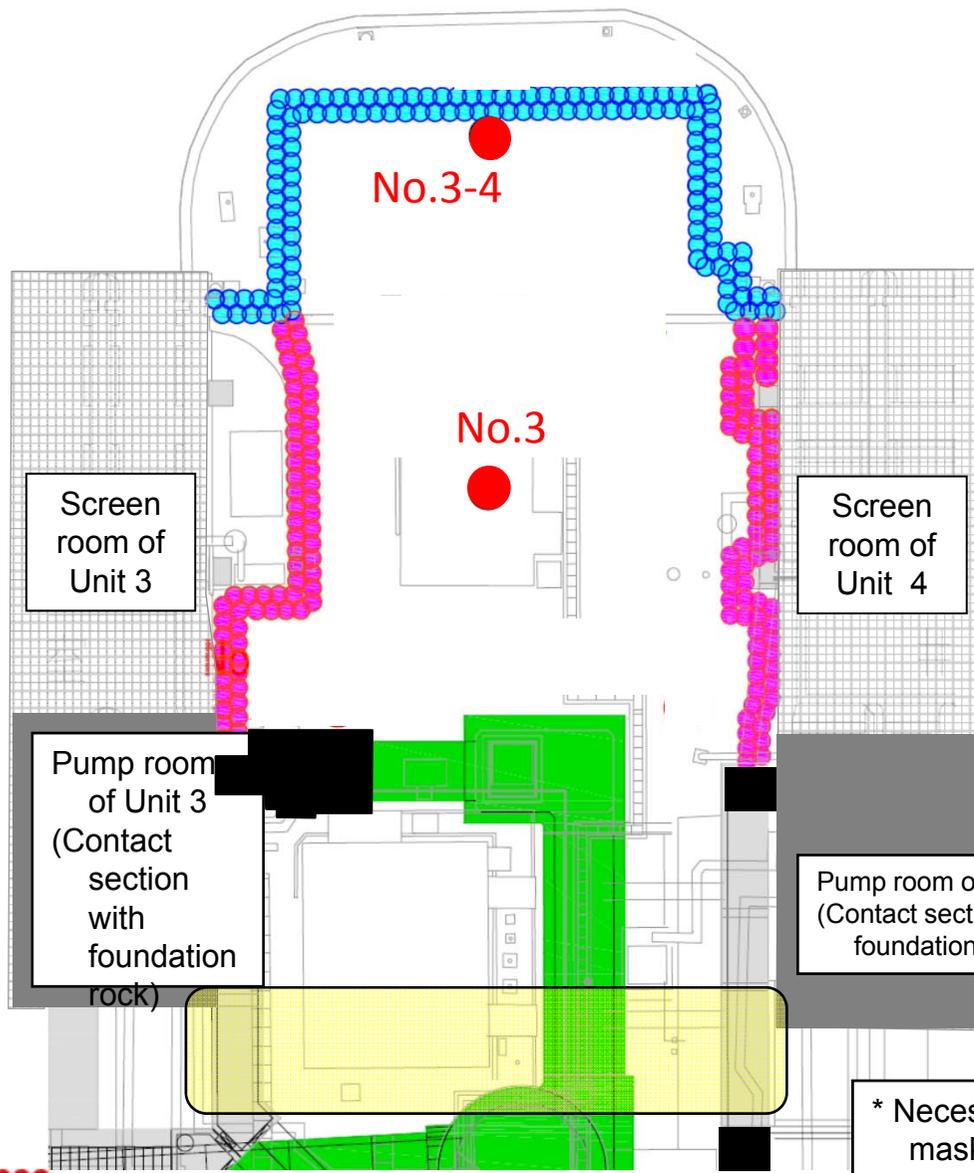

Ground improvement (sea side):
132 out of 132 locations
(construction started on August 23, 2013 and completed on January 23, 2014)

Ground improvement (mountain side):
137 out of 137 locations
(October 19, 2013-March 5, 2014)

* Necessity of ground improvement construction at the yellow masking area will be considered.
