

**Situation of Storing and Treatment of Accumulated Water including Highly Concentrated Radioactive Materials at Fukushima Daiichi Nuclear Power Station  
(6<sup>th</sup> Release)**

August 3, 2011

Tokyo Electric Power Company

**1. Purpose**

This document is to report the following matters in accordance with the instruction of “(Instruction) Regarding installment of treatment facility and storing facility of water including highly concentrated radioactive materials at Fukushima Daiichi Nuclear Power Station of the Tokyo Electric Power Company (NISA No. 6, June 8, 2011),” dated June 9.

<Instruction>

Situation of storing and treatment of the contaminated water in the Power Station and future forecast based upon the current situation have to be reported to NISA as soon as the treatment facility starts its operation. Also, subsequently, continued report has to be submitted to NISA once in a week until the treatment of the accumulated water in the Centralized Radiation Waste Treatment Facility is completed.

**2. Situation of storing and treatment of accumulated water in the building (actual record)**

Stored amount in each unit building (Unit 1 to 4 (including condenser and trench)), and stored and treated amount in the Accumulated Water Storing Facility (including underpass area close to the High Temperature Incinerator Building), and other related data, on August 2, are shown in the Attachment material-1.

**3. Future forecast of storing and treatment**

**(1) Short term forecast**

Water transfer is planned so that the level of the accumulated water in the Unit 1 and 2 building and Unit 3 and 4 building will not exceed OP. 4,000, taking the stored amount in the Accumulated Water Storing Facility and the operating situation of the radioactive material treatment equipment into consideration. Water is transferred to the Process Main Building in principle, by securing the enough capacity for accepting accumulated water in the Process Main Building.

Hence, priority for treatment is placed on the accumulated water in the Process Main Building in order to reserve the capacity for accepting the accumulated water in the building.

Stored amount in each unit building (Unit 1 to 4 (including condenser and trench)), and stored and treated amount in the Accumulated Water Storing Facility (including underpass area close to the High Temperature Incinerator Building), and other related data, forecasted on August 9, are shown in the Attachment material-2.

## **(2) Middle term forecast**

Regarding the accumulated water in the Unit 1 and 2 building and Unit 3 and 4 building, from the viewpoint of reducing the risks of discharging to the ocean and leaking into the groundwater, water transfer is planned with considering the capacity of the Process Main Building, by setting the intermediate target of the accumulated water level in the building at OP. 3,000, for the purpose of keeping enough reserve for the accumulated water level by reaching to OP. 4,000 and keeping the accumulated water level lower than the groundwater level.

Also, treatment of the accumulated water in the Process Main Building is planned taking the situation of installing the middle and low level waste water tanks, and the operation availability and maintenance period of the radioactive material treatment equipment into consideration.

On the other hand, the accumulated water level in the High Temperature Incinerator Building is kept below OP. 4,200, and the transfer is planned when certain amount of store capacity is reserved in the Process Main Building. Treatment of the accumulated water in the High Temperature Incinerator Building is carried out when enough store capacity of the Process Main Building is reserved for accepting the accumulated water in the High Temperature Incinerator Building.

Stored amount in each unit building (Unit 1 to 4 (including condenser and trench)), and storing and treatment situation in the Accumulated Water Storing Facility (including underpass area close to the High Temperature Incinerator Building), forecasted for 3 months, are shown in the Attachment material-3.

Stored amount in each building and the water storage equipment is forecasted to reduce through the transfer and treatment. According to the forecast for 3 months, water levels in the buildings of Unit 2 and 3 are estimated to decrease to OP. 3,000 after the beginning and the end of September respectively, supposing that there is no change in the water injection amount and no effect of rainfall, although the forecast could vary in accordance with the operation availability of the radioactive material treatment equipment, or other parameters.

Also, the water treated by the radioactive material treatment equipment can be stored in the middle and low waste water tanks, which are currently being installed.

END

# Storage and treatment of high level radioactive accumulated water (August 2, 2011)


Lines	
	High level radioactive water
	Treated water (saltwater)
	Treated water (concentrated saltwater)
	Treated water (freshwater)
	Freshwater

	Stored volume	Change from last report	Storage capacity
Freshwater receiving tank	21,055m <sup>3</sup>	+ 4,490m <sup>3</sup>	28,000m <sup>3</sup>
Freshwater receiving tank	1,197m <sup>3</sup> 1	-	5,000m <sup>3</sup>

	Chlorine Concentration	2
Before Desalination	6,600ppm	
After Desalination	20ppm	

1 Since desalination plant is operated and the water level is not still, the figure is a reference.

2 Data on 7/28

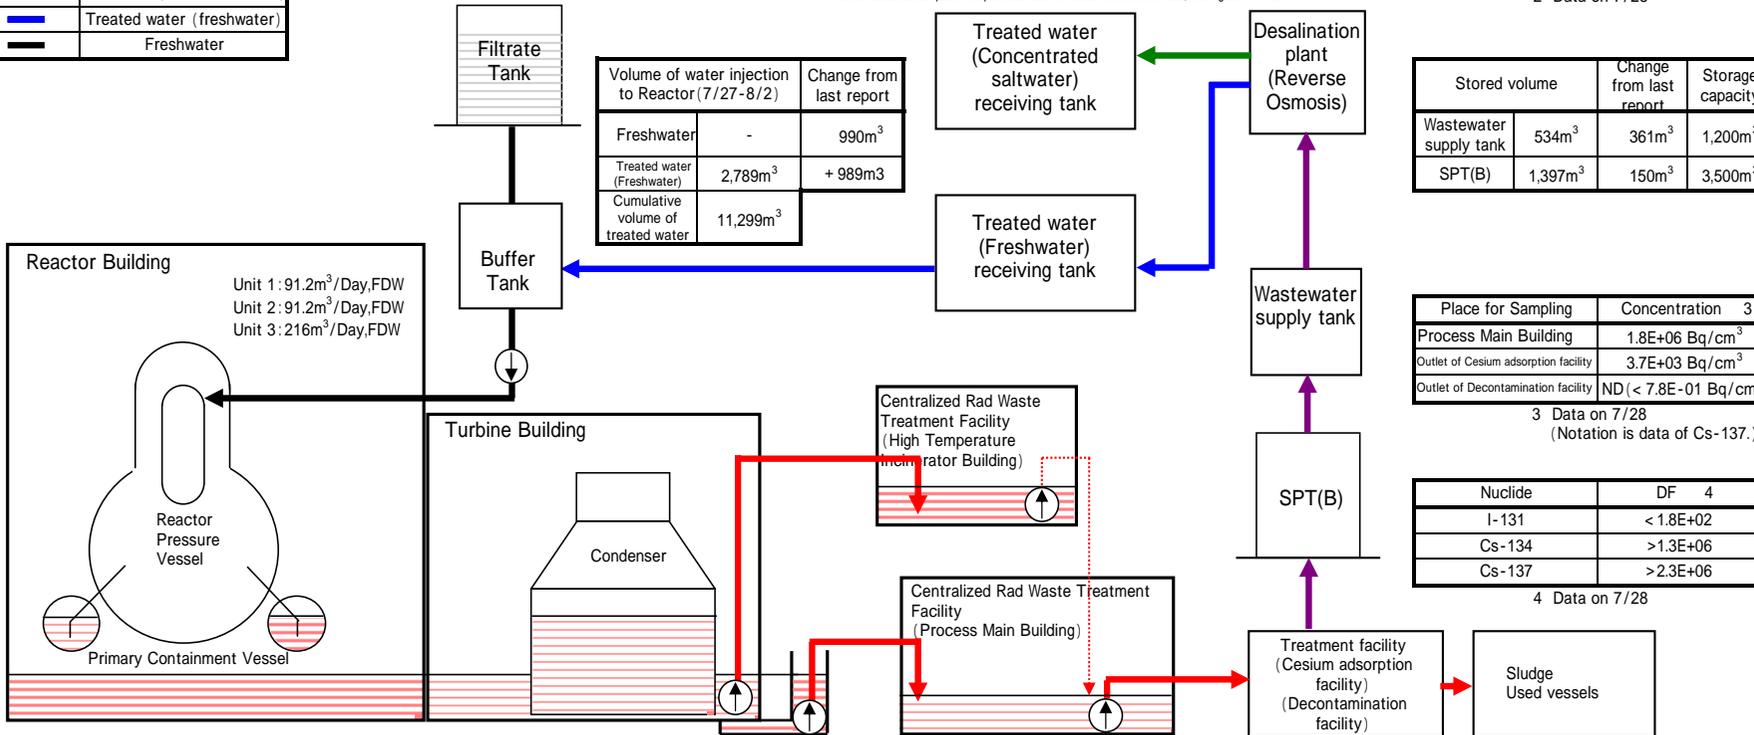

Volume of water injection to Reactor (7/27-8/2)		Change from last report
Freshwater	-	990m <sup>3</sup>
Treated water (Freshwater)	2,789m <sup>3</sup>	+ 989m <sup>3</sup>
Cumulative volume of treated water	11,299m <sup>3</sup>	

	Stored volume	Change from last report	Storage capacity
Wastewater supply tank	534m <sup>3</sup>	361m <sup>3</sup>	1,200m <sup>3</sup>
SPT(B)	1,397m <sup>3</sup>	150m <sup>3</sup>	3,500m <sup>3</sup>

Place for Sampling	Concentration	3
Process Main Building	1.8E+06 Bq/cm <sup>3</sup>	
Outlet of Cesium adsorption facility	3.7E+03 Bq/cm <sup>3</sup>	
Outlet of Decontamination facility	ND (< 7.8E-01 Bq/cm <sup>3</sup> )	

3 Data on 7/28  
(Notation is data of Cs-137.)

Nuclide	DF	4
I-131	< 1.8E+02	
Cs-134	> 1.3E+06	
Cs-137	> 2.3E+06	

4 Data on 7/28


Facility	Accumulated volume	Change from last report	Water level in Turbine Building	Transfer to
Unit 1	Approx. 17,320m <sup>3</sup>	60m <sup>3</sup>	OP.4.959	Process Main Building
Unit 2	Approx. 27,500m <sup>3</sup>	+ 200m <sup>3</sup>	OP.3.626	
Unit 3	Approx. 29,800m <sup>3</sup>	100m <sup>3</sup>	OP.3.585	Process Main Building
Unit 4	Approx. 22,300m <sup>3</sup>	100m <sup>3</sup>	OP.3.604	
Total	Approx. 96,920m <sup>3</sup>			

Storage facility	Accumulated volume	Change from last report	Water level	Treated volume (7/27-8/2)	Cumulative treated volume	Waste produced	Change from last report	Storage volume
Process Main Building	Approx. 19,010m <sup>3</sup>	+ 480m <sup>3</sup>	OP.5.337	Approx. 6,190m <sup>3</sup>	Approx. 35,310m <sup>3</sup>	Sludge	282m <sup>3</sup>	+ 49m <sup>3</sup>
HTI Building	Approx. 4,840m <sup>3</sup>	300m <sup>3</sup>	OP.3.424			Used vessels	101	+ 19
Total	Approx. 23,850m <sup>3</sup>							

**Note**

- Previous report: July 26, 2011
- On July 22 to 23 and 24 to 25, filtrate was supplied from Filtrate Tank to Buffer Tank.
- We continue transfer from Unit 2, 3 to Process Main Building. (We temporarily stopped transferring due to the adjustment of water level in the Process Main Building. (Unit 2: 7/29 9:43am ~ 7/30 4:10pm, Unit 3: 7/29 9:48am ~ 7/30 4:13pm: Temporary halt to the transferring))
- 7/29 10:03am ~ 4:09pm, 7/31 1:58pm ~ 8/1 10:21am: Transferring from High Temperature Incinerator Building to Process Main Building was done.

# Storage and treatment of high level radioactive accumulated water (Forecast for August 9, 2011)

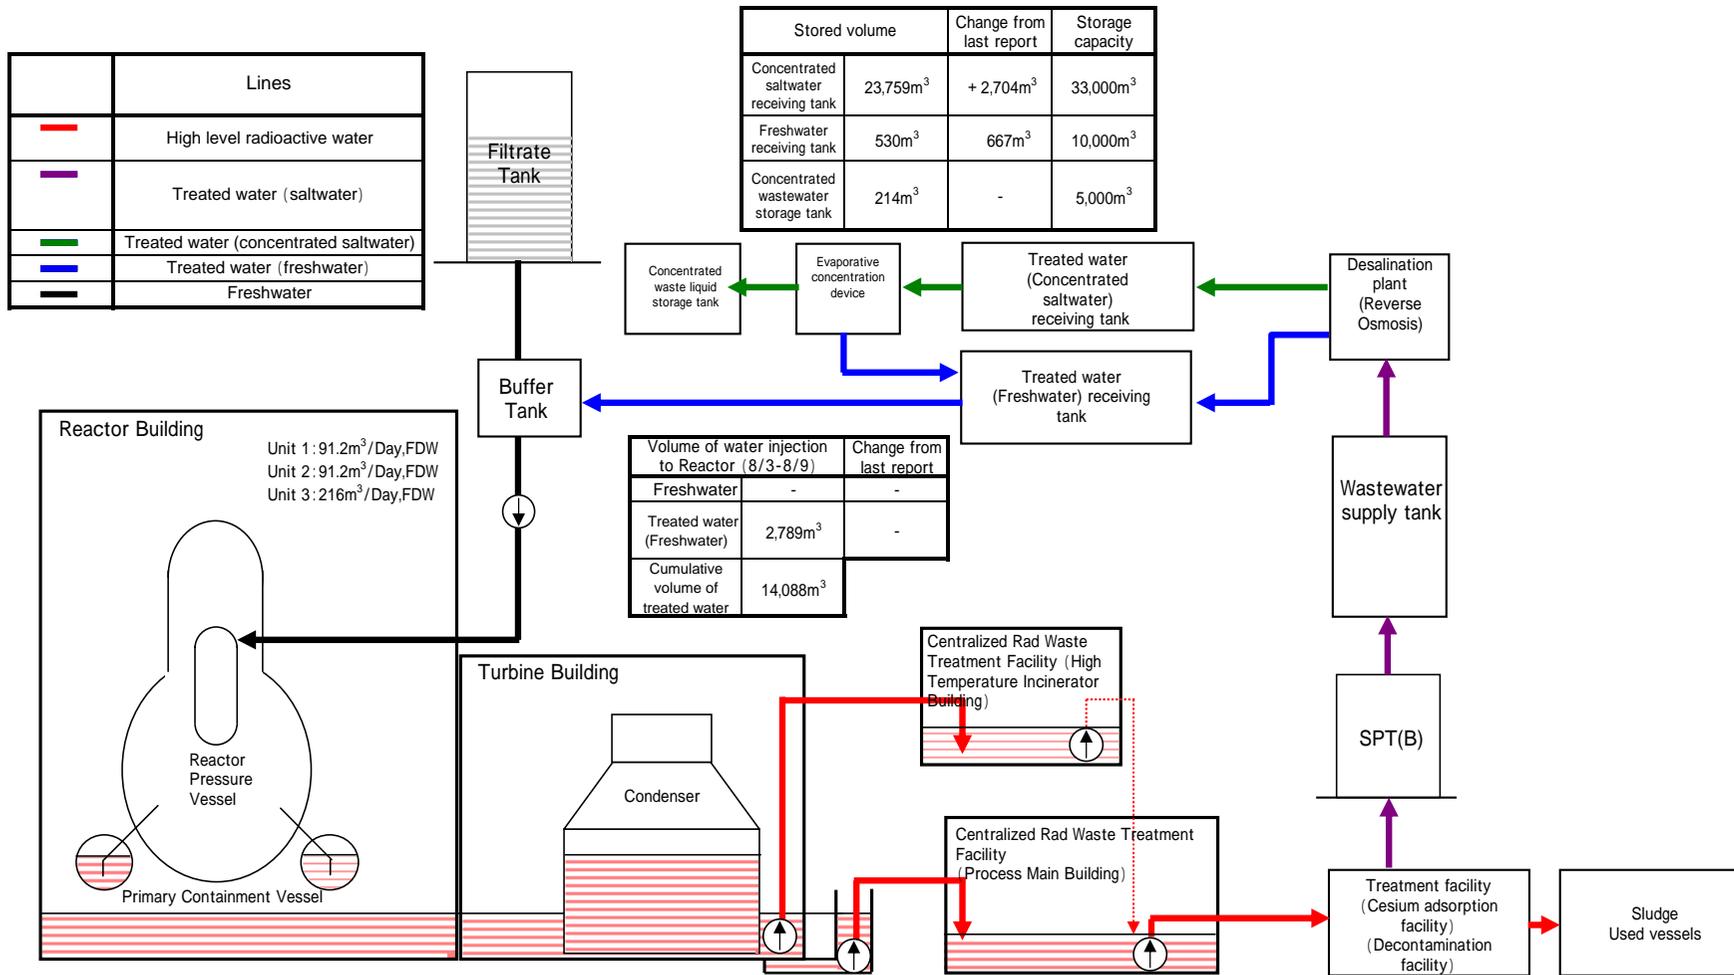


Facility	Accumulated volume	Change from last report	Water level in Turbine Building	Transfer to
Unit 1	Approx. 17,240m <sup>3</sup>	80m <sup>3</sup>	OP.3,611 (T/B of Unit 2)	Process Main Building
Unit 2	Approx. 27,400m <sup>3</sup>	100m <sup>3</sup>		Process Main Building
Unit 3	Approx. 29,500m <sup>3</sup>	300m <sup>3</sup>	OP.3,550 (T/B of Unit 3)	Process Main Building
Unit 4	Approx. 22,100m <sup>3</sup>	200m <sup>3</sup>		Process Main Building
<b>Total</b>	<b>Approx. 96,240m<sup>3</sup></b>			

Storage facility	Accumulated volume	Change from last report	Water level	Treated volume (8/3-8/9)	Cumulative treated volume	Waste produced		Change from now	Storage volume
						Sludge	Used vessels		
Process Main Building	Approx. 18,880m <sup>3</sup>	130m <sup>3</sup>	OP.5,303	Approx. 5,040m <sup>3</sup>	Approx. 40,350m <sup>3</sup>	322m <sup>3</sup>	113	+ 40m <sup>3</sup>	800m <sup>3</sup>
HTI Building	Approx. 5,050m <sup>3</sup>	+ 210m <sup>3</sup>	OP.3,599					12	192
<b>Total</b>	<b>Approx. 23,930m<sup>3</sup></b>								


**Note**

- We will continue to transfer from Unit 2 and 3 to Process Main Building.
- The capacity factor of the Treatment facility is assumed at 60%, taking account of the suspension of the treatment device due to countermeasure against reduction of flow volume.
- On August 7, the operation of the evaporative concentration device is planned to start.


Water Level of Accumulated Water, Unit2 (mm) (Unit 1&2 connected)

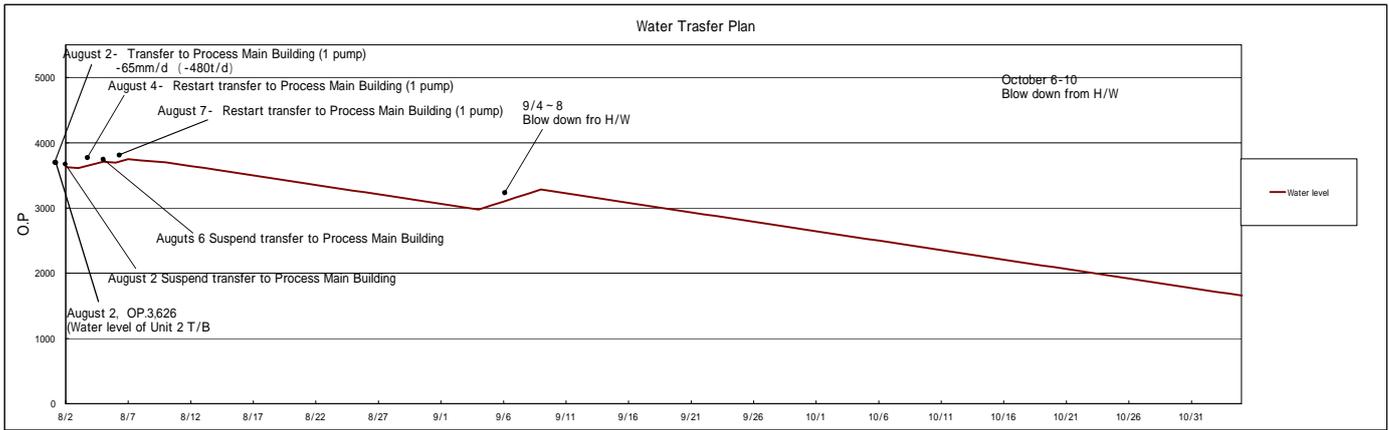


Water Level of Accumulated Water, Unit 3 (mm) (Unit 3&4 connected)

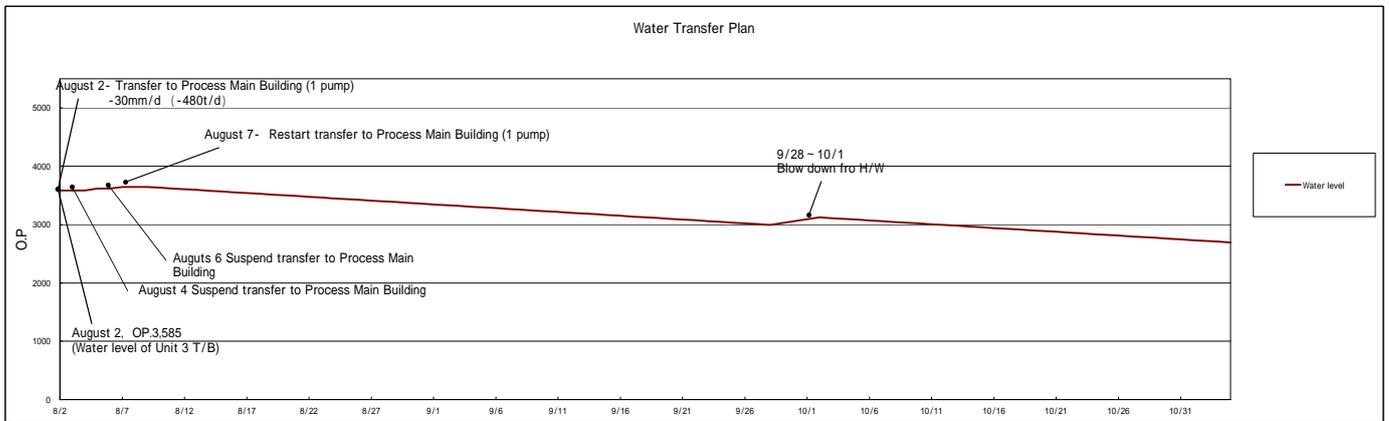

Stored Volume at Centralized R/W

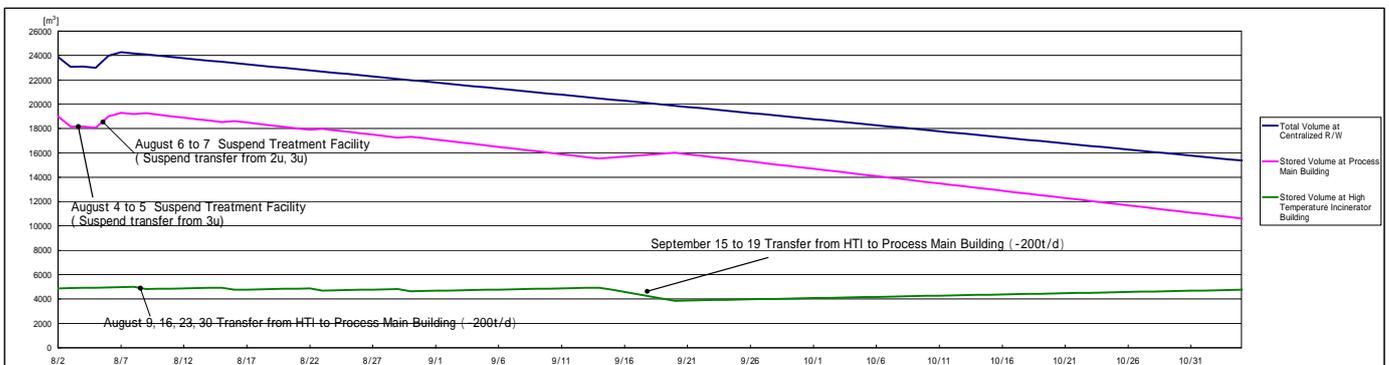

Tank Capacity of Treated Water (Concentrated Saltwater) and Stored Volume of Treated Water (Concentrated Saltwater)

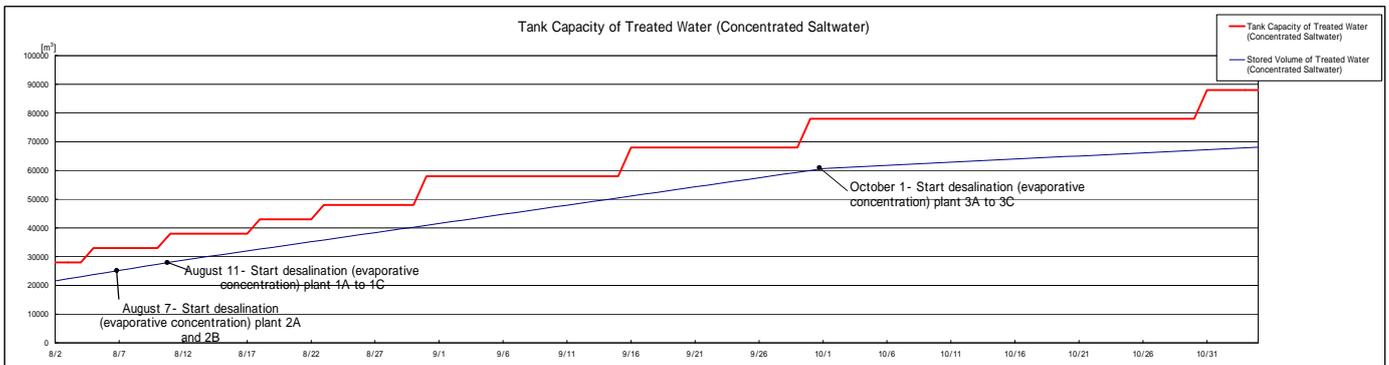

The assumed operation rate is 70% until the beginning of August and later then 90%.
