Situation of Storage and Treatment of Accumulated Water including Highly Concentrated Radioactive Materials at Fukushima Daiichi Nuclear Power Station (112th Release)

August 14, 2013

Tokyo Electric Power Company

1. Introduction

This document is to report the following matters in accordance with the instruction of "Installment of treatment facility and storing facility of water including highly concentrated radioactive materials at Fukushima Daiichi Nuclear Power Station of the Tokyo Electric Power Company (Instruction) "(NISA No. 6, June 8, 2011), dated on June 9, 2011.

<Instruction>

TEPCO should report to NISA the situation of storing and treatment of the contaminated water in the Power Station and future forecast based upon the current situation have to be reported to NISA as soon as the treatment facility starts its operation. Also, subsequently, continued report has to be submitted to NISA once a week until the treatment of the accumulated water in the Central Radioactive Waste Treatment Facility is completed.

2. Situation of storing and treatment of accumulated water in the building (actual record)

Stored amounts in each unit building (Units 1 to 4 (including condensers and trenches)), and stored and treated amount in the Accumulated Water Storing Facility (including underpass area close to the High Temperature Incinerator Building), and other related data, as of August 13, are shown in the Attachment -1.

3. Forecast of storing and treatment

(1) Short term forecast

Water transfer is planned so that the levels of the accumulated water in Units 1&2 and Units 3&4 building will be maintained around at the level of OP. 3,000, based on the stored amount in the Accumulated Water Storing Facilities and the operating situation of the radioactive material treatment equipment. Water is transferred to the Process Main Building and/or High Temperature Incinerator Building as Accumulated Water Storing Facilities.

Treatment is implemented considering the situation of storage and transfer of Accumulated Water Storing Facilities.

We assume stored amounts in each unit building (Units 1 to 4 (including condenser and trench)),

and stored and treated amount in the Accumulated Water Storing Facilities (including underpass area close to the High Temperature Incinerator Building), and other related data as of August 20, as shown in Attachment -2.

(2) Middle term forecast

Regarding accumulated water in Unit 1&2 building and Unit 3&4 building, from the viewpoint of reducing the risks of discharging to the ocean and leaking into the groundwater, it is necessary to keep enough capacity for the accumulated water in the building until its level reaches OP. 4,000 and to keep the accumulated water level lower than the groundwater level. On the other hand, based on the view of limiting inflow of underwater to buildings and reducing the amount of emerged accumulated water, we are planning to transfer accumulated water keeping its level in the building around OP. 3,000 considering water tank capacity.

As for accumulated water of the Process Main Building and the High Temperature Incinerator Building, we are planning to treat the accumulated water considering the situation of construction of middle and low level waste water tanks, the operation factor of the radioactive material treatment instruments and duration for maintenance.


We forecast stored amounts in each unit building (Unit 1 to 4 (including condensers and trenches)), and storing and treatment situations in the Accumulated Water Storing Facilities (including underpass areas close to the High Temperature Incinerator Building) for 3 months, as shown in Attachment -3.

Stored amounts in each building and the water storage equipment are forecasted to be unchanged in case transfer and treatment were implemented as scheduled without rain. However, it would be subject to change depending on the operation factor of the radioactive material treatment instruments and so on.

Also, the water treated at the radioactive material treatment equipment (fresh water and condensed salt water) can be stored in the middle and low level waste water tanks.

END

Storage and treatment of high level radioactive accumulated water (as of August 13, 2013)

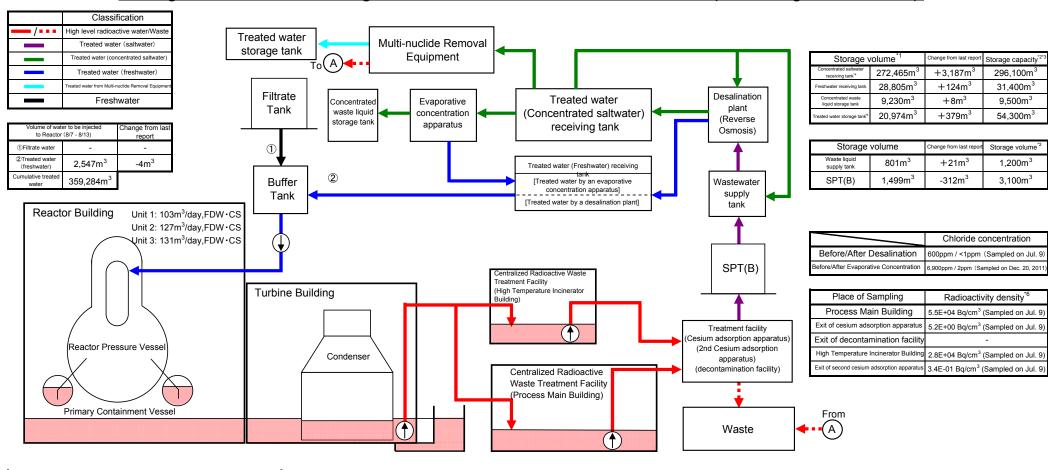

Facility	Storage	Change from	Water level in	
Facility	volume	last report	T/B	
Unit 1	Approx.13,900m ³	-100m ³	OP.2,919	
Unit 2	Approx.22,100m ³	-1,300m ³	OP.3,097	
Unit 3	Approx.22,900m ³	+300m ³	OP.2,964	
Unit 4	Approx.17,700m ³	+500m ³	OP.2,950	
Total	Approx.76.600m ³			

Storage Facility	Storage volume	Change from last report	Water level	Treated volume (8/7 - 8/13)	Cumulative treated volume	Waste	produced	Change from last report	Storage capacity
Process Main Building	Approx.12,930m ³	+130m ³	OP.3,363	Approx. 5,470m ^{3 *7}	Approx.712,660m ^{3 *7}	Sludge	597m ³	No change	700m ^{3 *2}
High Temperature Incinerator Building	Approx. 3,620m ³	+790m ³	OP.2,414			Used vessels	565 ^{*8}	+ 3	2,506
Total	Approx.16,550m ³					*1	The figures are just for	or reference when the water le	vel of Desalination System ar

*1 The figures are just for reference when the water level of Desalination System and Evaporative concentration apparatus are not stable.

*7 Total treated amount of Cesium adsorption apparatus and 2nd Cesium adsorption apparatus Breakdown of the treated amount: Cesium adsorption apparatus (0m³)

2nd Cesium adsorption apparatus (5,470m 3)

Equipment (49) and treated column (0)

Breakdown of the cumulative treated amount: Cesium adsorption apparatus (189,250m³) 2nd Cesium adsorption apparatus (523,410m 3)

*8 Breakdown of the used vessels:

[Highlights from the previous update (August 6, 2013) to the present status]

- Since August 12, water transfer from Unit 2 to Unit 3 Turbine Building has been under suspension
- Water transfer from Unit 3 to the High Temperature Incinerator Building is in progress.
- Since November 29, water transfer from Unit 4 has been under suspension.
- 2nd Cesium Adsorption Apparatus are under operation (Availability factor 65.1% (Projected: 65%)).
- Since July 17, Cesium Adsorption Apparatus has been under suspension.
- On August 9, groundwater was pumped up from the water collecing pit, which was installed at the east side of Unit 1,2 Turbine Building, and was transferred to Unit 2 vertical shaft.
- Storage capacity of the "concentrated saltwater receiving tank" and the "treated water storage tank" will be increased by adding tanks.

Cesium adsorption apparatus (434) 2nd cesium Cesium adsorption apparatus (82) Storage container of the Multi-nuclide Removal


^{*2} Shows the operational limit. *3 The underground reservoirs are not included in the figure.

^{*4} Storage capacity of the filtrate water tank (4,600m3) is included in the figure.

^{*5} The treated water from the Multi-nuclide Removal Equipment (under hot test) is stored. Freshwater and concentrated saltwater will be stored depending on the operation status.

^{*6} Data of Cs-137 are described above

Storage and treatment of high level radioactive accumulated water (August 20, 2013)

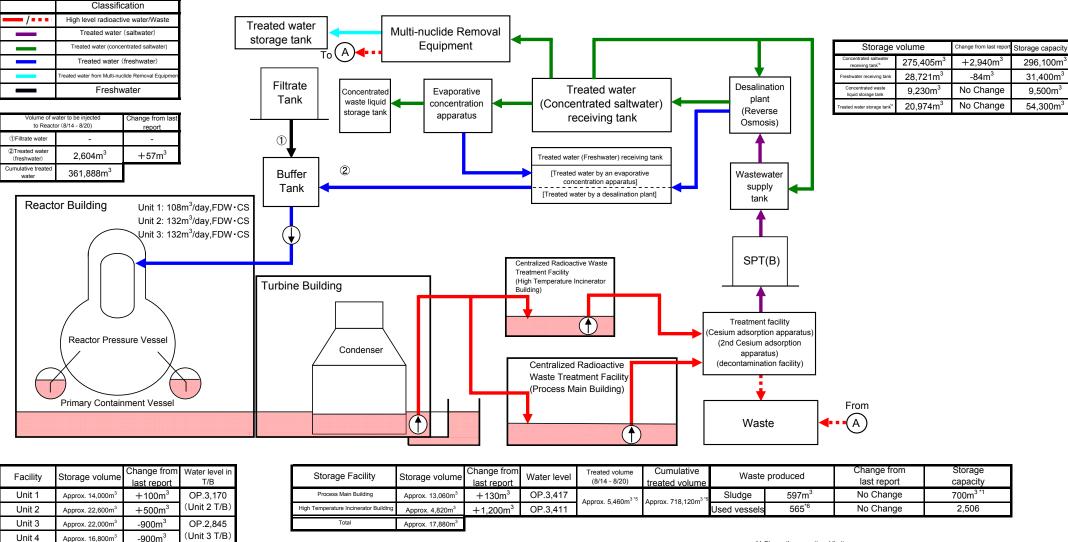

[Highlights from the present status (August 13, 2013) to the supposition status]

Approx. 75,400m³

Total

- *1 Shows the operational limit.
- *2 The underground reservoirs are not included in the figure.
- *3 Storage capacity of the filtrate water tank (4,600m3) is included in the figure.
- *4 The treated water from the Multi-nuclide Removal Equipment (under hot test) is stored.

 Freshwater and concentrated saltwater will be stored depending on the operation status.
- *5 Total treated amount of Cesium adsorption apparatus and 2nd Cesium adsorption apparatus

Breakdown of the treated amount: Cesium adsorption apparatus (0m³)

2nd Cesium adsorption apparatus (5.460m³)

Breakdown of the cumulative treated amount: Cesium adsorption apparatus (189,250m³)

*6 Breakdown of the used vessels

2nd Cesium adsorption apparatus (528,870m ³) Cesium adsorption apparatus (434) 2nd cesium Cesium adsorption apparatus (82) Storage container of the Multi-nuclide Removal Equipment (49) and treated column (0)

⁻ Water transfer from Unit 2 to the High Temperature Incinerator Building will be restarted. Destination of water transfer from Unit 2 will be switched from the High Temperature Incinerator Building to the Unit 3 Turbine Building.


⁻ Water transfer from Unit 3 to the High Temperature Incinerator Building will be conducted


⁻ Water transfer from Unit 4 will be stopped continuously.


Operation of 2nd Cesium Absorption Apparatus is scheduled: Availability Factor 65% (Projected)


Cesium Absorption Apparatus will be stopped continuously.

Simulation Results of Accumulated Water Treatment in Unit 1-4 T/B









Note

- The treated water volume is assumed to be 780m³/d (Subject to change depending on the level of water accumulated in T/B).
- The accumulated water level in T/B is a simulation result in consideration of flactuation of water level such as recent rainfall, inflow of groundwater, and etc.

⁻ The accumulated water level in T/B is assumed to increase by 5mm daily, taking into consideration the average rain fall in the surrounding area of Fukushima Daiichi Nuclear Power Station (August-October in the past 3 years).
