
Changes in the amount of water transferred from groundwater drains to reactor and turbine buildings and in the amount of groundwater and rainwater flowing into the buildings

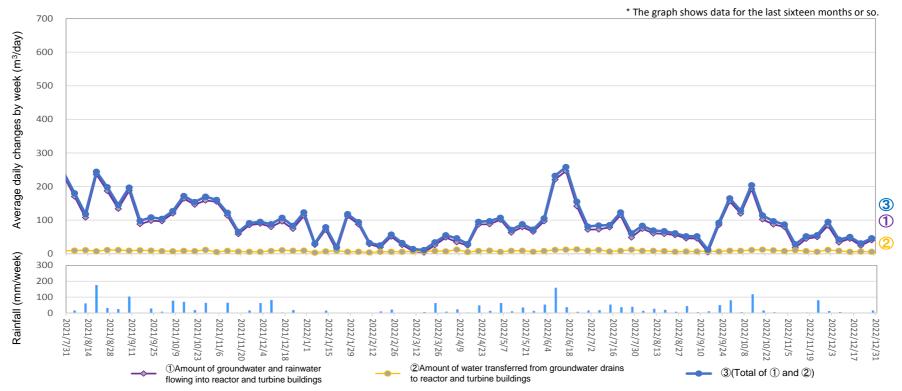

Amount of water transferred from groundwater drains to reactor and turbine buildings (From December 22, 2022 to December 28, 2022)


| Date | Temporary storage tanks | | | |
|--------------------------|-------------------------|---|---|-----------|
| | Α | В | С | Total (α) |
| From Dec 22 to Dec 28 | 0 | 0 | 0 | 0 |

| | | | | [m³/day] |
|----------------------|--|----------------------|-----------|---|
| (Re | (Reference) improved wells and well points | | | |
| Between Units 1-2 | Between Units 2-3 | Between Units 3-4 | Total (β) | Amount of water transferred to turbine buildings $[(\alpha)+(\beta)]$ |
| 6 | 0 | 0 | 6 | 6 |

^{*} ①Amount of groundwater and rainwater flowing into reactor and turbine buildings: 40 m³/day, ②Amount of water transferred from groundwater drains to reactor and turbine buildings: 6 m³/day, ③(Total of ① and ②): 46 m³/day, Rainfall: 14.5 mm/week


^{*} There may be a difference between the sum of the individual data and the total value since the total value is the sum of the data with the first decimal place.

(Reference) Changes in the amount of water transferred from groundwater drains to reactor and turbine buildings and in the amount of groundwater and rainwater flowing into the buildings from the start of measurement

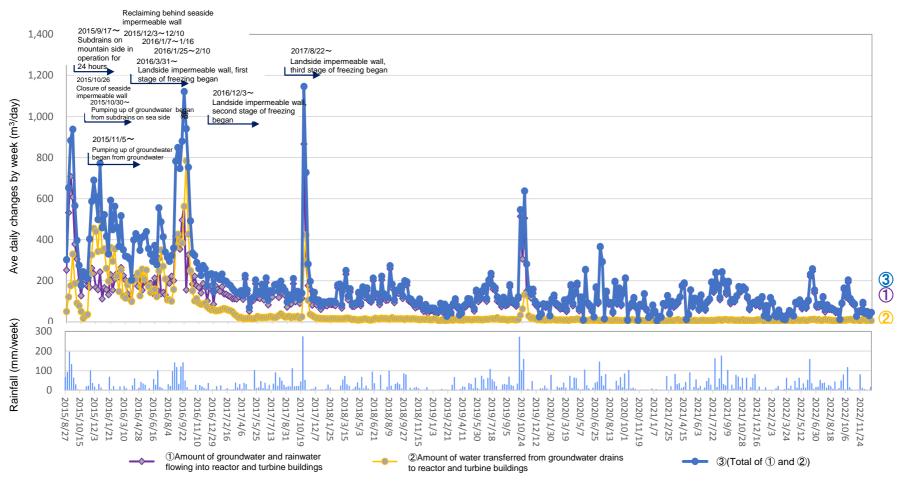

[m³/dav]

Changes in the amount of water transferred from groundwater drains to reactor and turbine buildings and in the amount of groundwater and rainwater flowing into the buildings

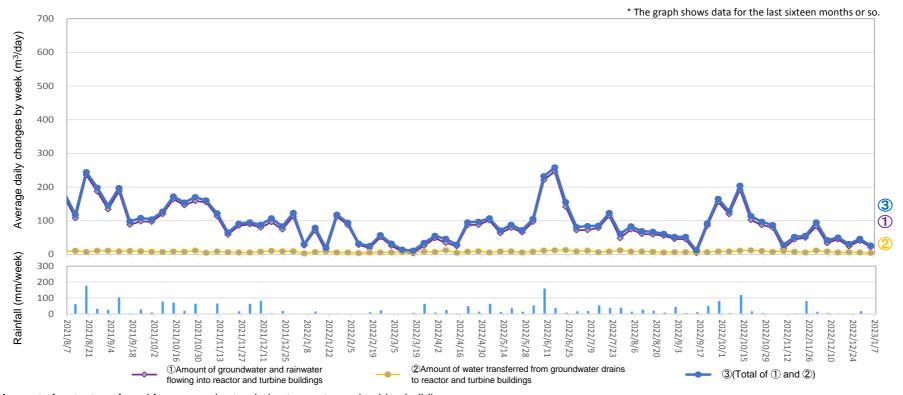

Amount of water transferred from groundwater drains to reactor and turbine buildings (From December 29, 2022 to January 4, 2023)

| Date | Temporary storage tanks | | | |
|-------------------------|-------------------------|---|---|-----------|
| | Α | В | С | Total (α) |
| From Dec 29 to Jan 4 | 0 | 0 | 0 | 0 |

| (Reference) improved wells and well points | | | | (Reference) |
|--|----------------------|----------------------|-----------|---|
| Between Units 1-2 | Between Units 2-3 | Between Units 3-4 | Total (β) | Amount of water transferred to turbine buildings $[(\alpha)+(\beta)]$ |
| 5 | 0 | 0 | 5 | 5 |

^{*} ①Amount of groundwater and rainwater flowing into reactor and turbine buildings: 22 m³/day, ②Amount of water transferred from groundwater drains to reactor and turbine buildings: 5 m³/day, ③(Total of ① and ②): 26 m³/day, Rainfall: 0 mm/week

^{*} There may be a difference between the sum of the individual data and the total value since the total value is the sum of the data with the first decimal place.

(Reference) Changes in the amount of water transferred from groundwater drains to reactor and turbine buildings and in the amount of groundwater and rainwater flowing into the buildings from the start of measurement

