
[m³/dav]

Changes in the amount of water transferred from groundwater drains to reactor and turbine buildings and in the amount of groundwater and rainwater flowing into the buildings

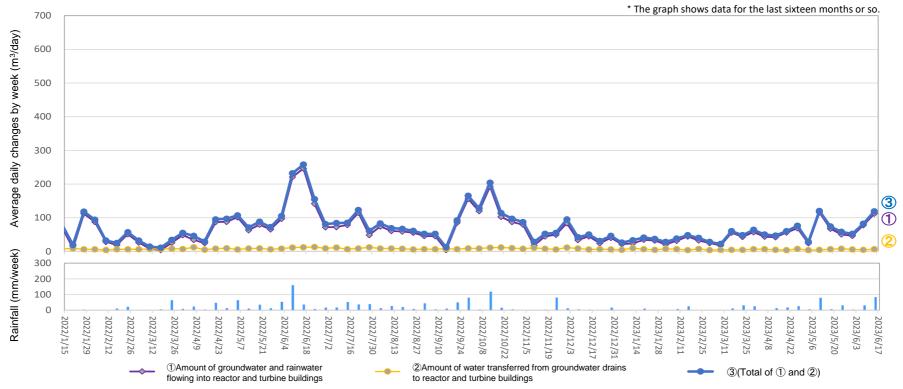

Amount of water transferred from groundwater drains to reactor and turbine buildings (From June 8, 2023 to June 14, 2023)

Date	Temporary storage tanks				
	Α	В	С	Total (α)	
From Jun 8 to Jun 14	0	0	0	0	

[/ 4.4						
(Re	(Reference)					
Between Units 1-2	Between Units 2-3	Between Units 3-4	Total (β)	Amount of water transferred to turbine buildings $[(\alpha)+(\beta)]$		
7	0	0	7	7		

^{*} ①Amount of groundwater and rainwater flowing into reactor and turbine buildings: 112 m³/day, ②Amount of water transferred from groundwater drains to reactor and turbine buildings: 7 m³/day, ③(Total of ① and ②): 119 m³/day, Rainfall: 81.5 mm/week

^{*} There may be a difference between the sum of the individual data and the total value since the total value is the sum of the data with the first decimal place.

(Reference) Changes in the amount of water transferred from groundwater drains to reactor and turbine buildings and in the amount of groundwater and rainwater flowing into the buildings from the start of measurement

