Reference

Radioactivity Density of the Seawater in the Port of Fukushima Daiichi NPS<1/2>

(Data summarized on September 30)

Place of Sampling	Shallow Draft	: Quay at F	- ukushima Daiich	i NPS*	Inside Unit 1-4 Water Intake Canal (North) at Fukushima Daiichi NPS (North side of the East Seawall Break)		Unit 1 Water Intake Canal at Fukushima Daiichi NPS (In front of Impermeable Wall)		Unit 2 Water Intake Canal at Fukushima Daiichi NPS (In front of Impermeable Wall)		Seawater at Unit 4 Screen		② Density Limit Specified by the Reactor Regulation
Time of Sampling	Sep 29, 2014 7:19 AM		N/A		Sep 29, 2014 7:00 AM		Sep 29, 2014 7:15 AM		Sep 29, 2014 7:12 AM		Sep 29, 2014 7:05 AM		(Bq/L) (The density limit in the water outside the
Detected Nuclides (Half-life)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	surrounding monitored areas is provided in section 6 of Appendix 2.)
I-131 (Approx. 8 days)	ND	-	-	-	ND	-	ND	-	ND	-	ND	-	40
Cs-134 (Approx. 2 years)	ND	-	-	-	3.6	0.06	4.1	0.07	5.1	0.09	7.9	0.13	60
Cs-137 (Approx. 30 years)	4.9	0.05	-	-	13	0.14	17	0.19	17	0.19	19	0.21	90

^{*} The density specified by the Reactor Regulation is converted from Bq/cm^3 to Bq/L. * Data of other nuclides is under evaluation.

As the detection limit may vary depending on the detectors and sample properties, there are cases where nuclides below the detection limit are detected.

^{*} In the case of more than 2 nuclides, the sum of scaling factors to density limits is compared to 1.

^{* &}quot;ND" indicates that the measurement result is below the detection limit.

I-131: Approx. 2Bq/L, Cs-134: Approx. 4Bq/L

^{*} The sampling will be performed after opening and closing of the silt fence.

Reference

Radioactivity Density of the Seawater in the Port of Fukushima Daiichi NPS<2/2>

(Data summarized on September 30)

Place of Sampling	Inside Unit 1-4 Water Intake Canal (South) at Fukushima Daiichi NPS (in front of Impermeable Wall)			ushima Daiichi N	In Front of Unit 6* Water Intake Canal at Fukushima Daiichi NPS						② Density Limit Specified by the Reactor Regulation (Bq/L) (The density limit in the water outside the surrounding monitored		
Time of Sampling	Sep 29, 2014 7:07 AM		N/A		N/A		Sep 29, 2014 7:30 AM						
Detected Nuclides (Half-life)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	areas is provided in
I-131 (Approx. 8 days)	ND	-	-	-	-	-	ND	-					40
Cs-134 (Approx. 2 years)	2.8	0.05	-	-	-	-	ND	-					60
Cs-137 (Approx. 30 years)	16	0.18	-	-	-	-	ND	-					90

^{*} The density specified by the Reactor Regulation is converted from Bq/cm^3 to Bq/L. * Data of other nuclides is under evaluation.

As the detection limit may vary depending on the detectors and sample properties, there are cases where nuclides below the detection limit are detected.


^{*} In the case of more than 2 nuclides, the sum of scaling factors to density limits is compared to 1.

^{* &}quot;ND" indicates that the measurement result is below the detection limit.


I-131: Approx. 2Bq/L, Cs-134: Approx.2Bq/L, Cs-137: Approx.2Bq/L

^{*} The sampling will be performed after opening and closing of the silt fence.


Radioactivity Density of the Seawater in Front of the Shallow Draft Quay at 1F (Bq/L)

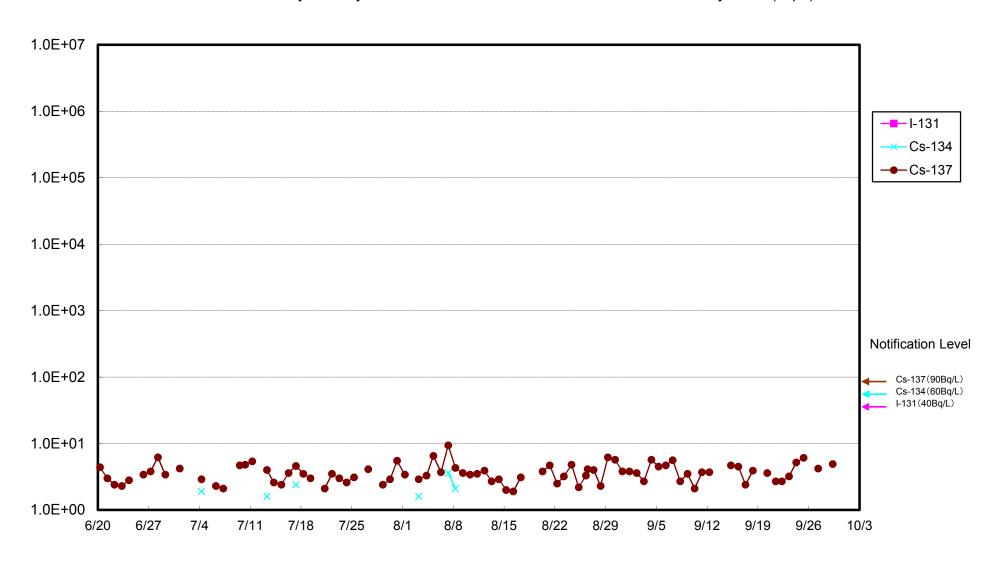


Radioactivity Density of the Seawater at the North of Unit 1-4 Water Intake (North of East Seawater Break of Fukushima Daiichi NPS (Bq/ L)

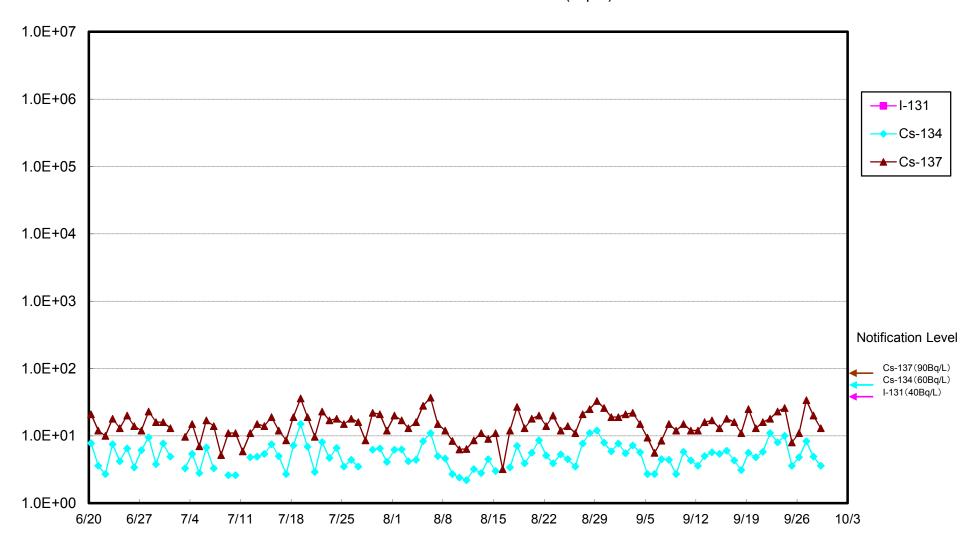


Radioactivity Density of the Seawater of Unit 1 Water Intake Canal at Fukushima Daiichi NPS (In front of Impermeable Wall) (Bq/L)

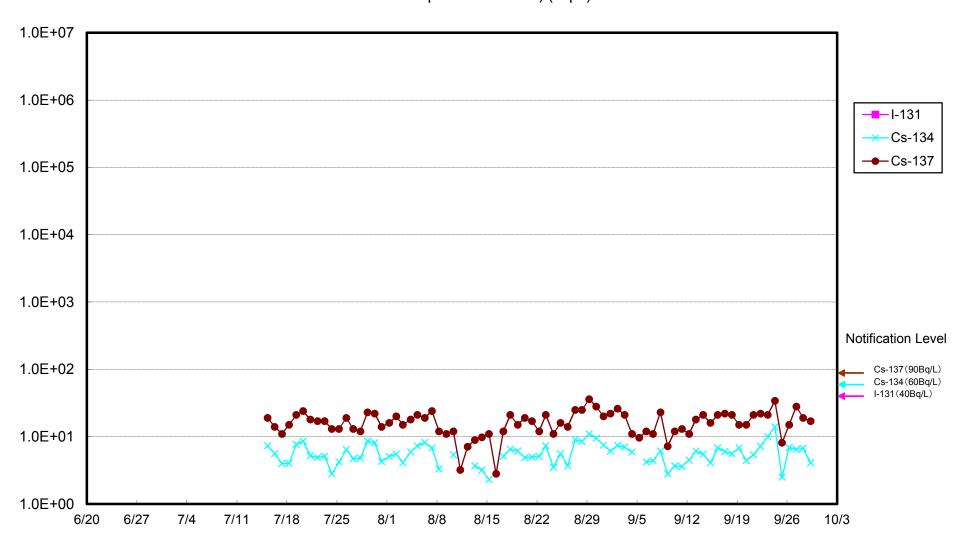


Radioactivity Density of the Seawater of Unit 2 Water Intake Canal at Fukushima Daiichi NPS (In front of Impermeable Wall) (Bq/L)

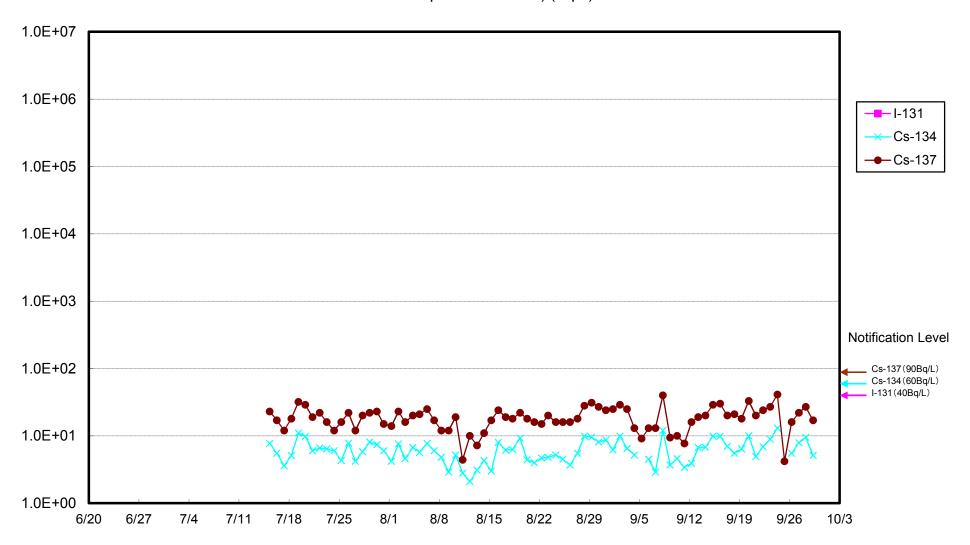

Radioactivity Density of the Seawater at Unit 4 Screen at Fukushima Daiichi NPS (Bq/L)

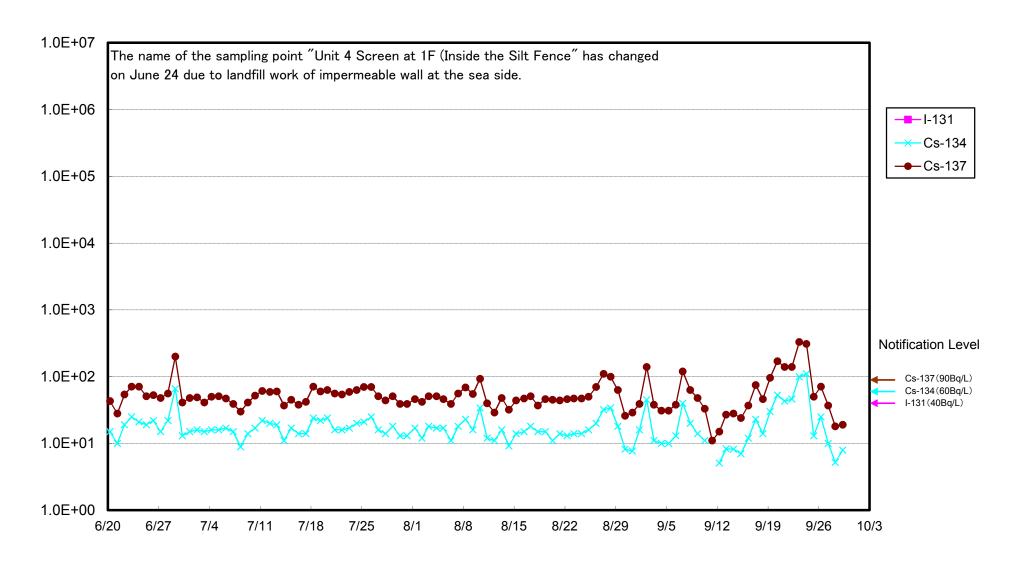

Radioactivity Density of the Seawater at the South of Unit 1-4 Water Intake (in front of Impermeable Wall) at Fukushima Daiichi NPS (Bq/L)

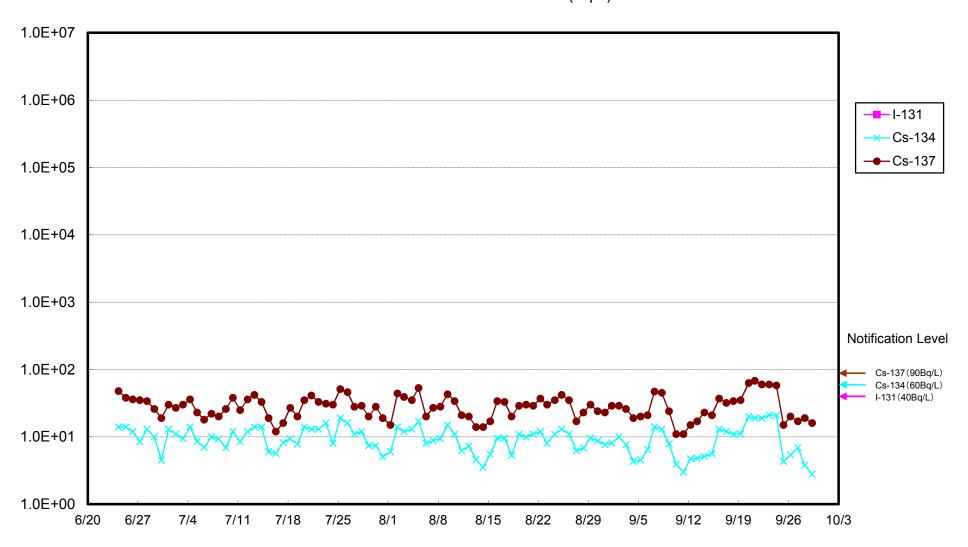

Radioactive Density of the Seawater in Front of Unit 6 Water Intake at Fukushima Daiichi NPS (Bq/L)

