Reference

Radioactivity Density of the Seawater in the Port of Fukushima Daiichi NPS<1/2>

(Data summarized on October 14)

Place of Sampling	Shallow Draft	t Quay at F	Fukushima Daiich	ni NPS*	Inside Unit 1-4 Water Intake Canal (North) at Fukushima Daiichi NPS (North side of the East Seawall Break)		Unit 1 Water Intake Canal at Fukushima Daiichi NPS (In front of Impermeable Wall)		Unit 2 Water Intake Canal at Fukushima Daiichi NPS (In front of Impermeable Wall)		Seawater at Unit 4 Screen		② Density Limit Specified by the Reactor Regulation
Time of Sampling	Oct 13, 2014 7:07 AM		N/A		Oct 13, 2014 7:32 AM		Oct 13, 2014 7:12 AM		Oct 13, 2014 7:15 AM		Oct 13, 2014 7:25 AM		(Bq/L) (The density limit in the water outside the
Detected Nuclides (Half-life)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	surrounding monitored areas is provided in section 6 of Appendix 2.)
I-131 (Approx. 8 days)	ND	-	-	-	ND	-	ND	-	ND	-	ND	-	40
Cs-134 (Approx. 2 years)	ND	-	-	-	4.3	0.07	6.5	0.11	4.1	0.07	3.9	0.07	60
Cs-137 (Approx. 30 years)	2.4	0.03	-	-	14	0.16	16	0.18	16	0.18	17	0.19	90

^{*} The density specified by the Reactor Regulation is converted from Bq/cm^3 to Bq/L. * Data of other nuclides is under evaluation.

As the detection limit may vary depending on the detectors and sample properties, there are cases where nuclides below the detection limit are detected.

^{*} In the case of 2 nuclides or more, the sum of scaling factors to density limits is compared to 1.

* "ND" indicates that the measurement result is below the detection limit.

I-131: Approx. 2Bq/L Cs-134: Approx.2Bq/L,

^{*} The sampling will be performed after opening and closing of the silt fence.

Reference

Radioactivity Density of the Seawater in the Port of Fukushima Daiichi NPS<2/2>

(Data summarized on October 14)

Place of Sampling	Inside Unit 1-4 Water Intake Canal (South) at Fukushima Daiichi NPS (in front of Impermeable Wall)						In Front of Unit 6 Water Intake Canal at 1F		Port Center at Fukushima Daiichi NPS				② Density Limit Specified by the Reactor Regulation
Time of Sampling	Oct 13, 2014 7:19 AM		N/A		N/A		Oct 13, 2014 7:02 AM		Oct 13, 2014 7:29 AM				(Bq/L) (The density limit in the water outside the
Detected Nuclides (Half-life)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	①Density of Sample (Bq/L)	Scaling Factor (①/②)	①Density of Sample (Bq/L)	Scaling Factor (1)/2)	surrounding monitored areas is provided in section 6 of Appendix 2.)
I-131 (Approx. 8 days)	ND	-	-	-	-	-	ND	-	ND	-			40
Cs-134 (Approx. 2 years)	4.5	0.08	-	-	-	-	ND	-	ND	-			60
Cs-137 (Approx. 30 years)	15	0.17	-	-	-	-	ND	-	5.2	0.06			90

^{*} The density specified by the Reactor Regulation is converted from Bq/cm^3 to Bq/L. * Data of other nuclides is under evaluation.

As the detection limit may vary depending on the detectors and sample properties, there are cases where nuclides below the detection limit are detected. *


^{*} In the case of 2 nuclides or more, the sum of scaling factors to density limits is compared to 1.

^{* &}quot;ND" indicates that the measurement result is below the detection limit.


I-131: Approx. 2Bq/L, Cs-134: Approx.3Bq/L Cs-137: Approx.3Bq/L

^{*} At these points, sampling is carried out once a week. (As for the port entrance, also sampled on the day the silt fence was opened/shut or covering work was carried out in the port.)


Radioactivity Density of the Seawater in Front of the Shallow Draft Quay at 1F (Bq/L)

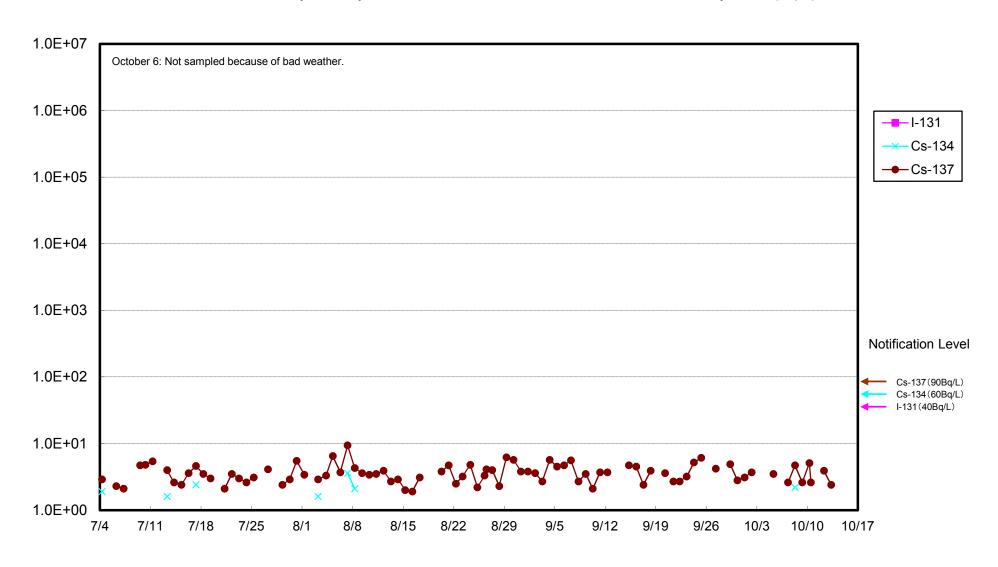


Radioactivity Density of the Seawater at the North of Unit 1-4 Water Intake (North of East Seawater Break of Fukushima Daiichi NPS (Bq/ L)

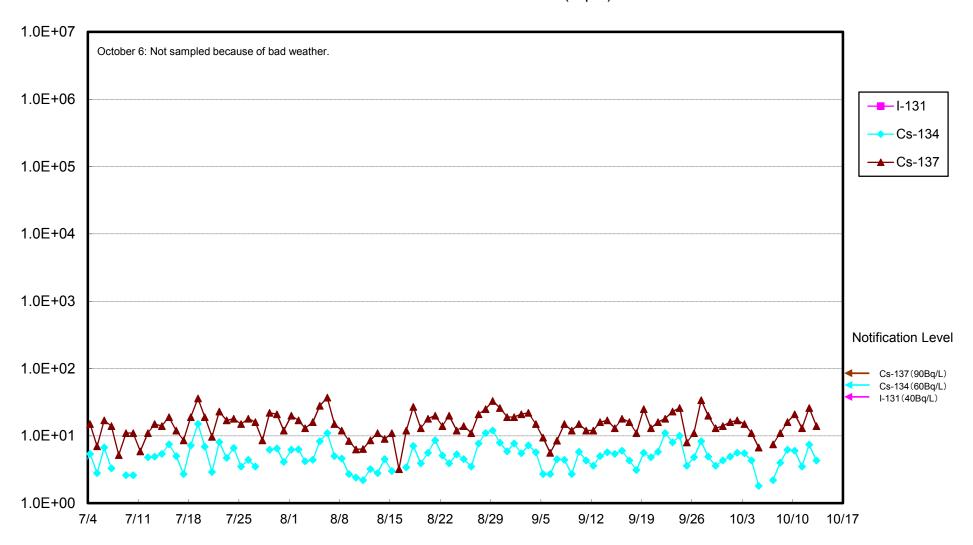


Radioactivity Density of the Seawater of Unit 1 Water Intake Canal at Fukushima Daiichi NPS (In front of Impermeable Wall) (Bq/L)

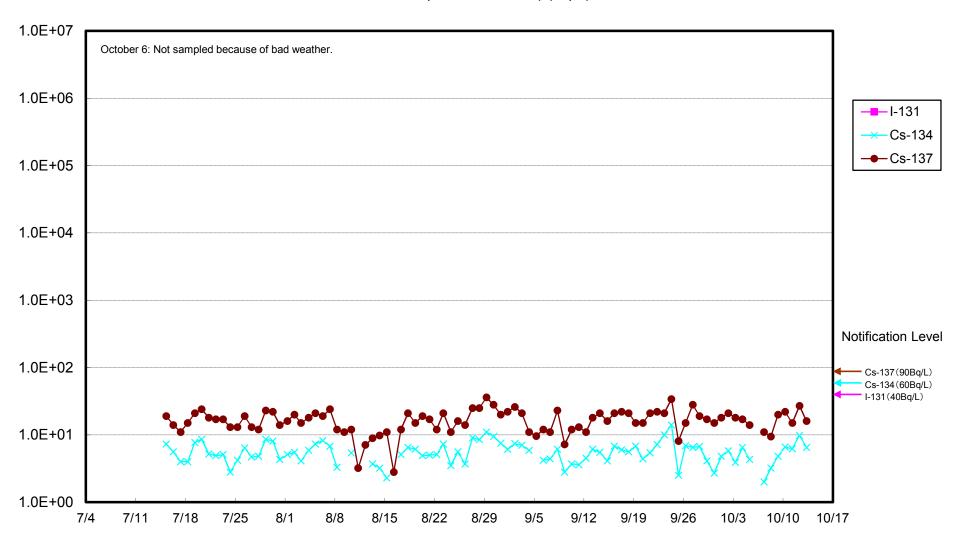


Radioactivity Density of the Seawater of Unit 2 Water Intake Canal at Fukushima Daiichi NPS (In front of Impermeable Wall) (Bq/L)

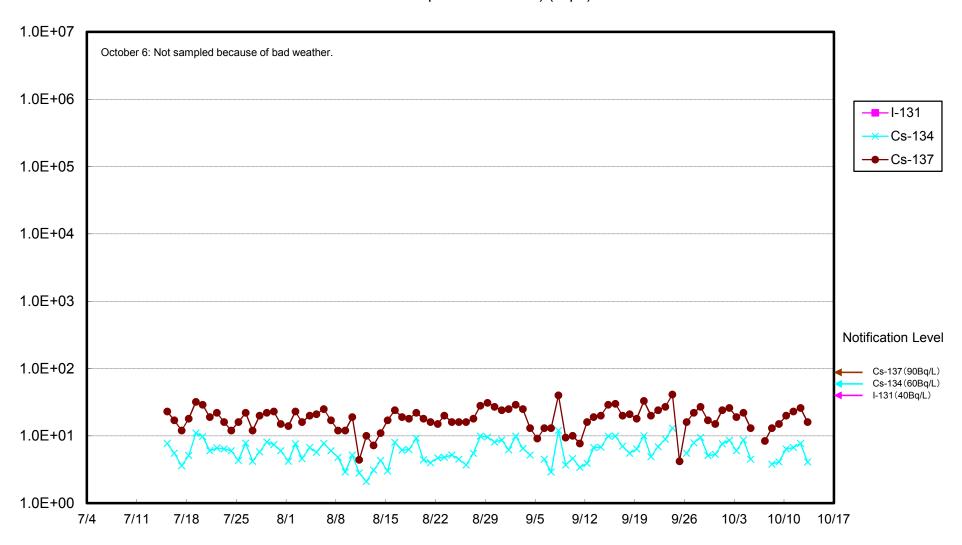


Radioactivity Density of the Seawater at Unit 4 Screen at Fukushima Daiichi NPS (Bq/L)

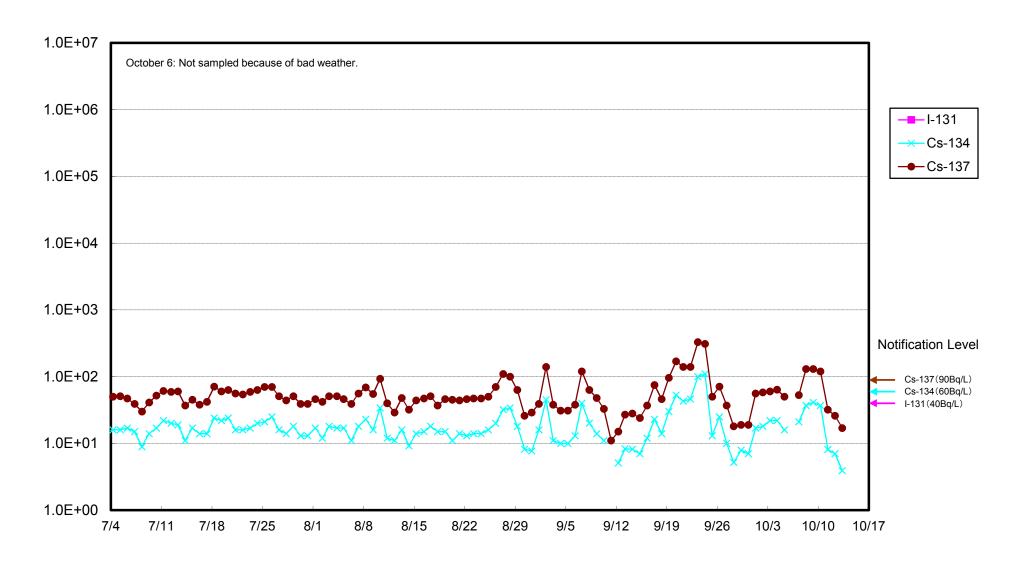

Radioactivity Density of the Seawater at the South of Unit 1-4 Water Intake (in front of Impermeable Wall) at Fukushima Daiichi NPS (Bq/L)

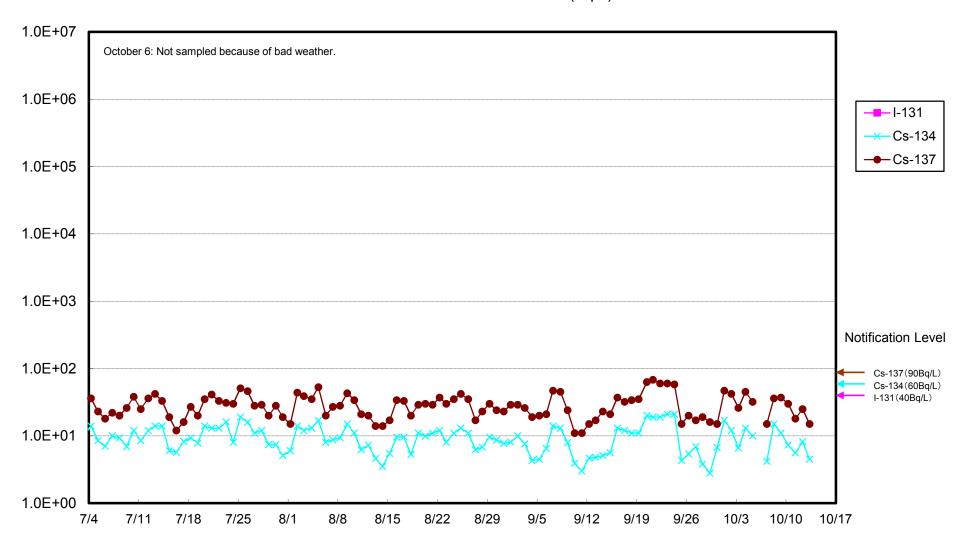

Radioactive Density of the Seawater in Front of Unit 6 Water Intake at Fukushima Daiichi NPS (Bq/L)

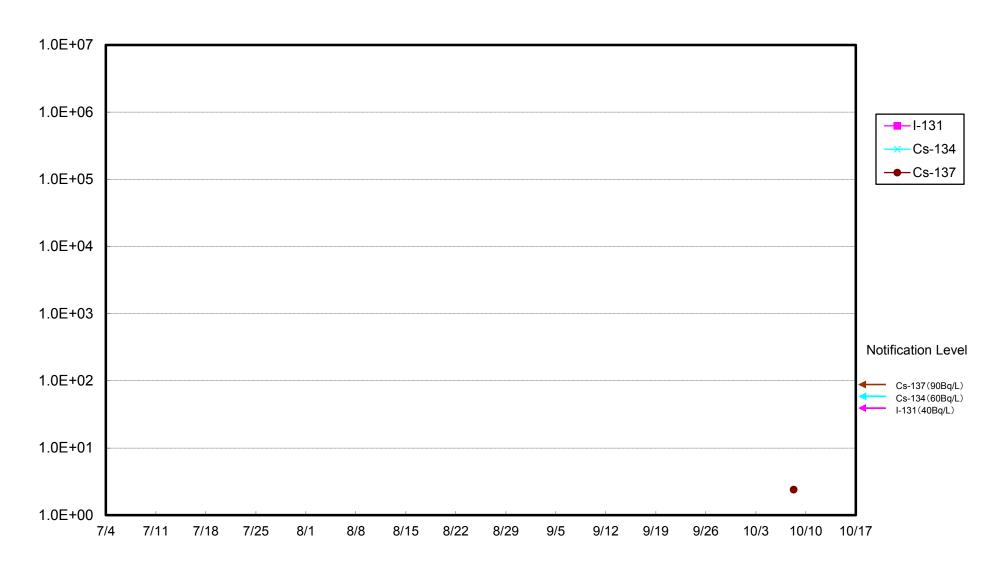

Radioactive Density of the Seawater in Port Center at Fukushima Daiichi NPS (Bq/L)

