

<Reference>


**Progress Status of the Ground Improvement/
Historical Data of Radioactive Density in
Groundwater at the East Side of Turbine Buildings**

**December 26, 2014
Tokyo Electric Power Company**

To prevent outflow of contaminated water into the port, ground improvement construction is undergoing at the east side of Unit 1-4 Turbine Buildings.

Results of radioactive nuclide analysis are published for the samples of groundwater at the east side of Unit 1-4 Turbine Buildings and seawater at the port in order to monitor the source and the extent of the radioactive materials in the groundwater, and whether the materials included in groundwater affect the sea.

● Sampling locations of underground water obtained at bank protection

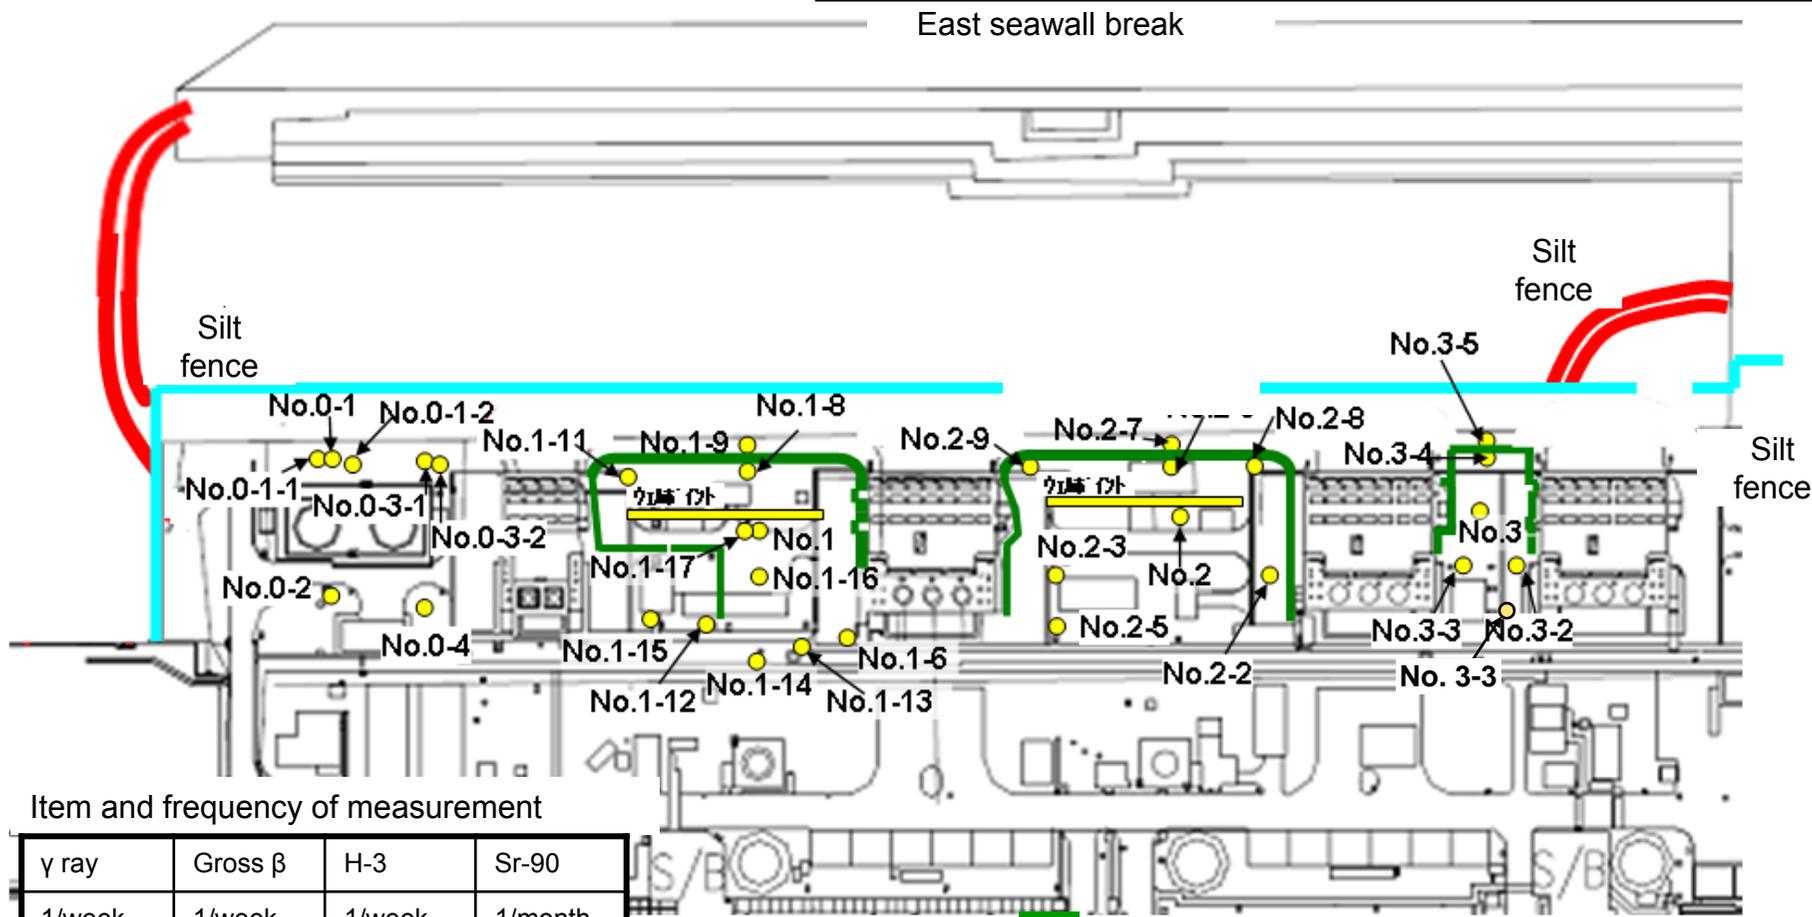

Item and frequency of measurement

γ ray	Gross β	H-3	Sr-90
1/week	1/week	1/week	1/month


* Frequency of the measurement is subject to change as needed.

○ Seaside impermeable wall


— : Location where ground improvement construction was completed (as of April 18, 2014)




Progress Status of Ground Improvement Construction between Units 1 and 2 (As of the Morning on December 26)

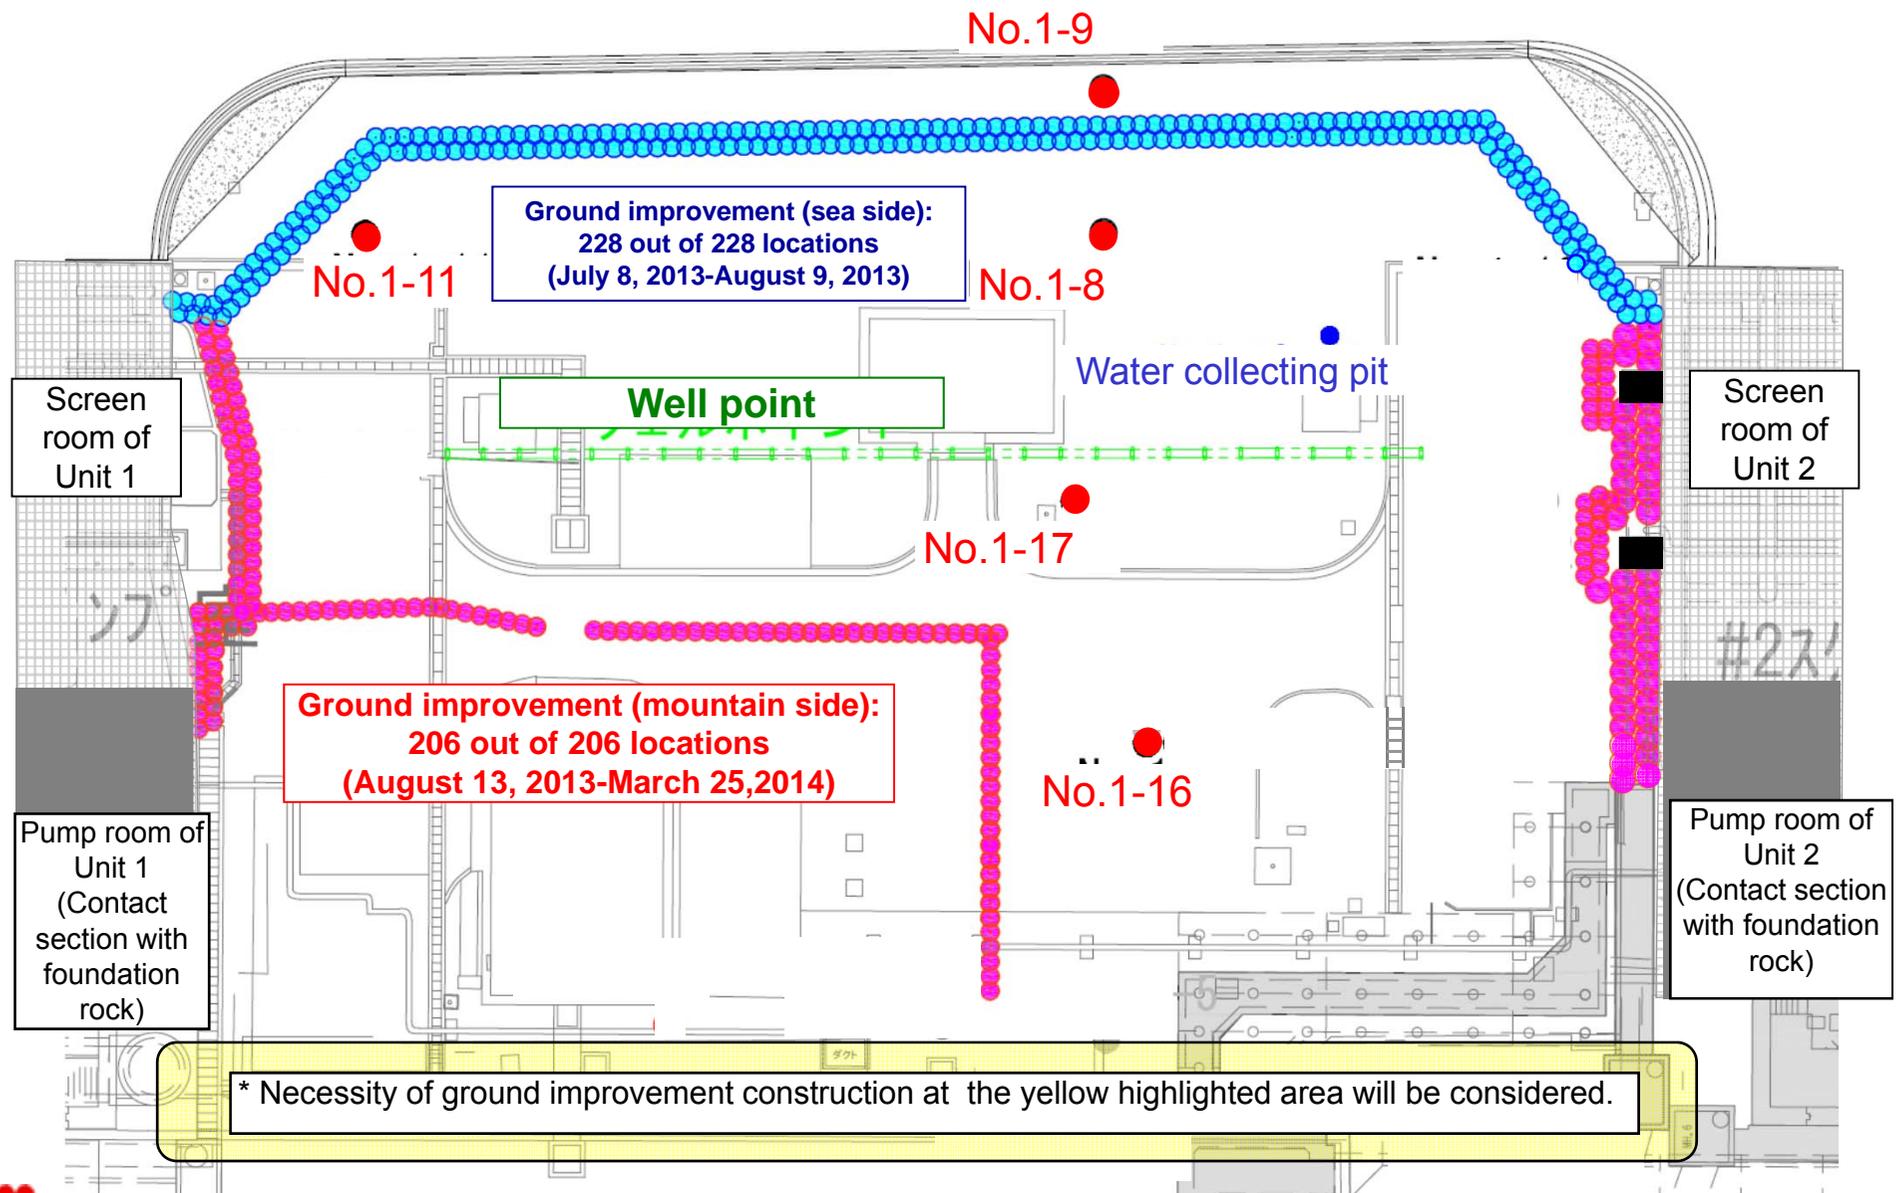

Progress Status of Ground Improvement Construction between Units 2 and 3 (As of the Morning on December 26)

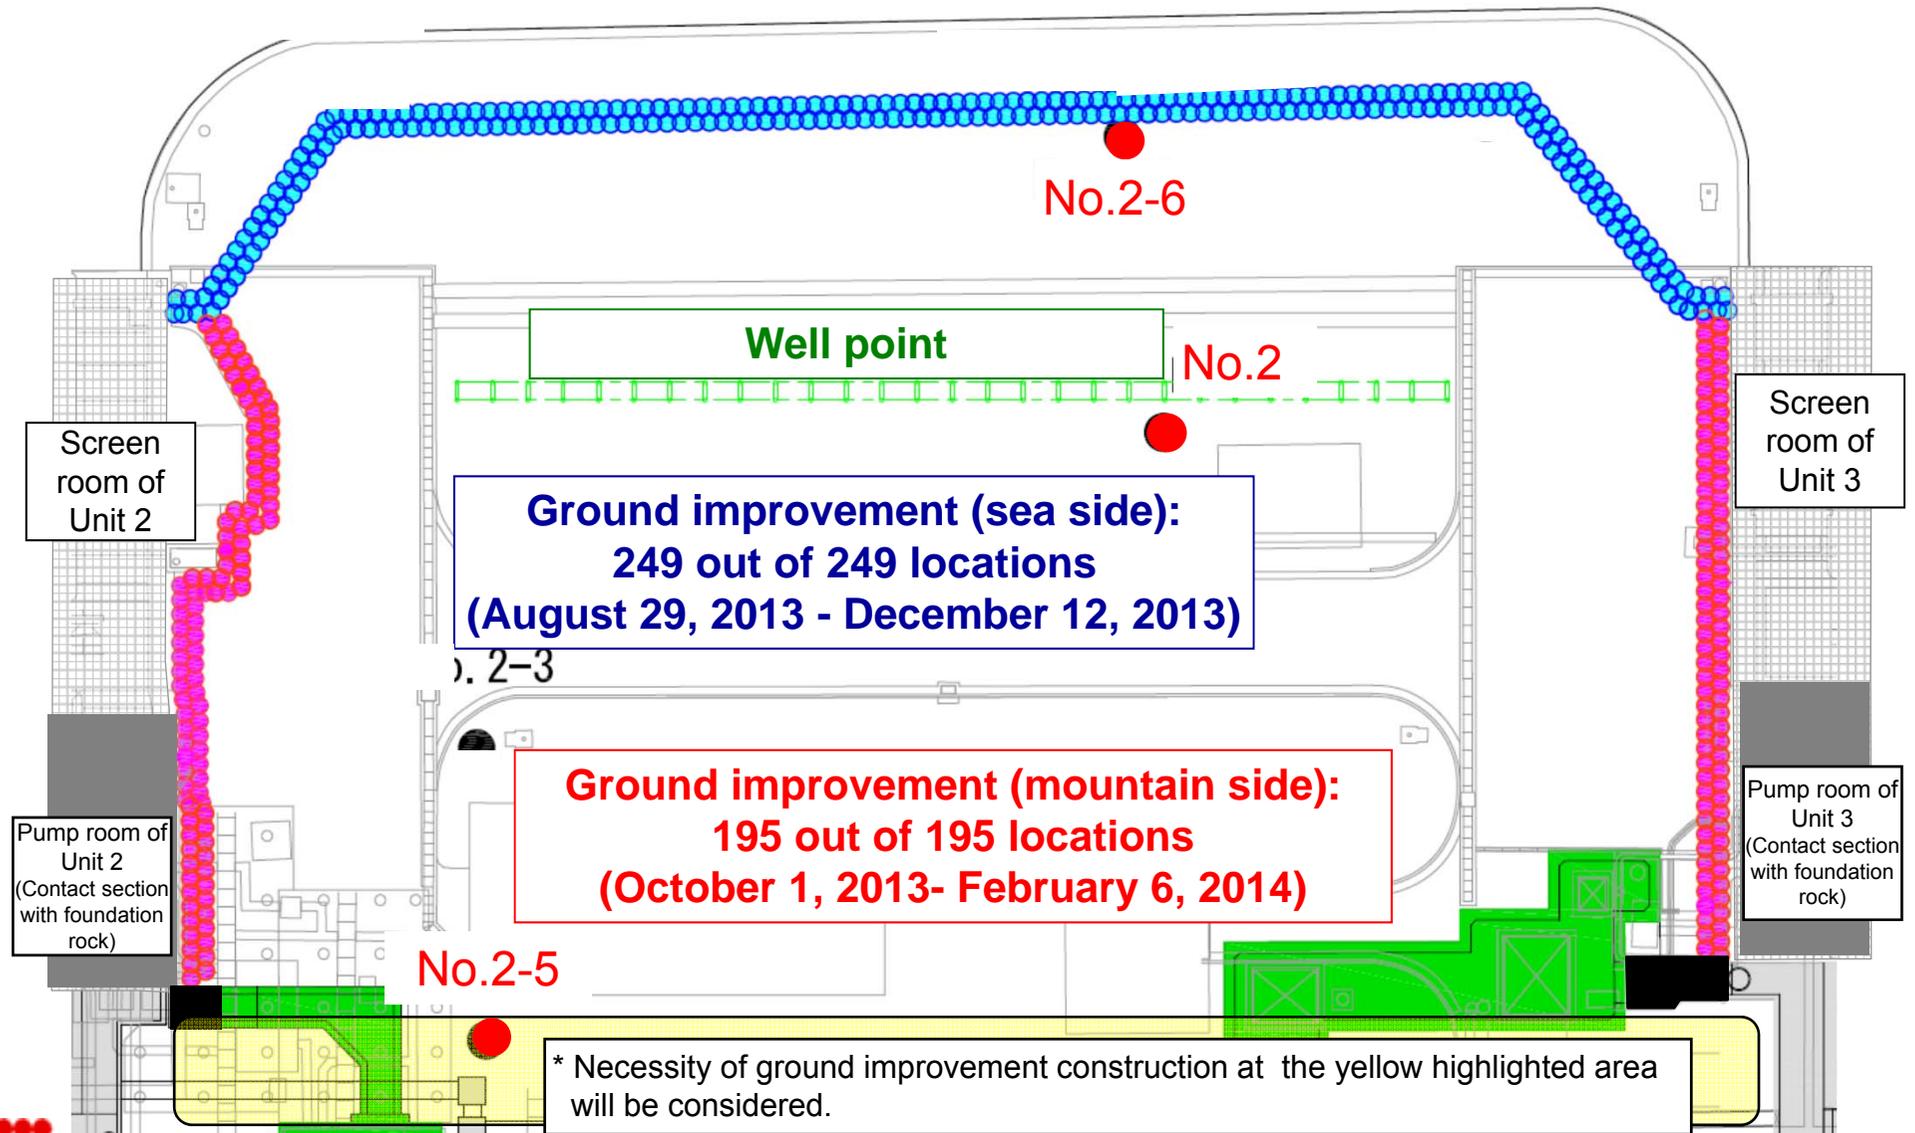

Progress Status of Ground Improvement Construction between Units 3 and 4 (As of the Morning on December 26)

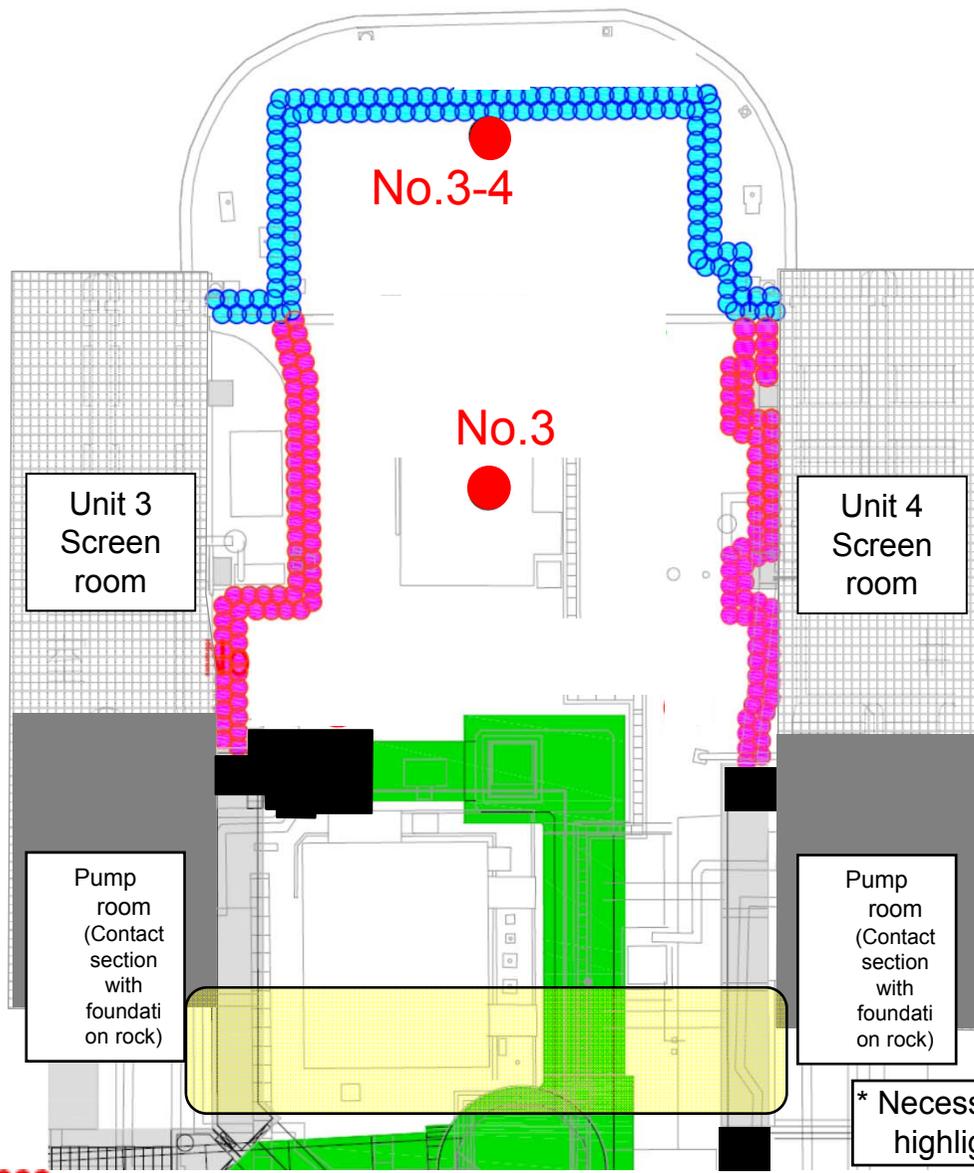

**Ground improvement (sea side):
132 out of 132 locations
(August 23, 2013 - January 23, 2014)**

**Ground improvement (mountain side):
137 out of 137 locations
(October 19, 2013- March 5, 2014)**

* Necessity of ground improvement construction at the yellow highlighted area will be considered.
