

# Fukushima Daiichi Nuclear Power Station

## Completion of the Seventh Discharge of ALPS Treated Water in FY2025

- The Seventh discharge of ALPS treated water in FY2025 began at 10:11 AM on March 6.
- In order to ensure that the ALPS treated water (tritium) is properly diluted every day during the discharge period, we have analyzed the tritium concentration in the water after dilution with seawater and confirmed that the analysis values are approximately equal to calculated concentrations, and below 1,500Bq/liter.
- During the discharge period, seawater samples have also been taken from 10 locations within 3km radius and 4 locations within 10km square of the power station, and the detection limit has been raised to approximately 10Bq/liter in order to quickly obtain tritium concentration measurement results. As a result, we have confirmed that the analysis values are below both the discharge suspension level (700 Bq/liter<sup>\*1</sup> or 30 Bq/liter<sup>\*2</sup>) and the investigation level (350 Bq/liter<sup>\*1</sup> or 20 Bq/liter<sup>\*2</sup>).

\*1 10 locations within 3 km of the power station

\*2 4 locations within 10 km square in front of the power station

< Announced by March 23, 2026 >

- During the Seventh discharge of ALPS treated water in FY2025, the amount of the ALPS treated water being discharged remained constant at approximately 460m<sup>3</sup>/day, and daily quick analysis results of tritium concentrations in the seawater have confirmed that the ALPS treated water is being discharged safely as planned.
- We completed the discharge of the ALPS treated water from the measurement/confirmation facility tank group B at 3:13 PM on March 23. The flush out of the water remaining in the ALPS treated water transfer line (ALPS treated water) was completed at 12:06 PM on March 24, and the completion of this task marked the end of the Seventh discharge of ALPS treated water in FY2025. (Total amount of water discharged: approx. 7,834 m<sup>3</sup>, Total amount of tritium discharged: Approx. 2.0 T Bq)
- Going forward, we will remain vigilant to ensure the safe and stable discharge of ALPS treated water.

- For the number of annual discharges, annual amount of water to be discharged, and annual amount of tritium to be discharged, the discharge results up to FY2025 and the discharge plan (draft) for FY2026 are as follows.

### [Discharge results up to FY2025]

	Annual number of discharges	Annual amount of water to be discharged [m <sup>3</sup> ]	Annual amount of tritium to be discharged [Bq]
FY2023	4	31,145	Approx. 4.5 T
FY2024	7	54,999	Approx. 12.7 T
FY2025	7	55,011	Approx. 16.0 T

### [discharge plan for FY2026 (draft)]

	Annual number of discharges	Annual amount of water to be discharged [m <sup>3</sup> ]	Annual amount of tritium to be discharged [Bq]
FY2026	8	62,400	Approx. 11 T

# [Reference] FY2025 ALPS treated water discharge plan (1/2)



- The FY2025 discharge plan is as follows. There will be seven discharges during the year with each discharge approximately 7,800m<sup>3</sup> for an annual amount of water to be discharged approximately 54,600m<sup>3</sup>. The annual amount of tritium to be discharged will be approximately 15 T Bq.

Management number <sup>※1</sup>	Transfer source tank <sup>※2</sup>	Amount of water to be transferred <sup>※3</sup>	Discharge commencement period	
25-1-12	G4 south area Group B (Transferred to Measurement/Confirmation facility group A) K3 area Group A/B <sup>※5</sup> (Transferred to Measurement/Confirmation facility group A)	<u>Approx. 8,080m<sup>3</sup></u> <sup>※4</sup> <u>Approx. 910m<sup>3</sup></u>	Secondary treatment: None Sum of the ratios to regulatory concentrations: 0.45 - 0.55 <sup>※6</sup> Tritium concentration: 220,000~370,000 Bq/liter <sup>※7</sup> Total tritium volume: Approx. 2.8 T Bq	April
25-2-13	K3 area Group A/B <sup>※5</sup> (Transferred to Measurement/Confirmation facility group C) J1 area Group E (Transferred to Measurement/Confirmation facility group C)	<u>Approx. 6,970m<sup>3</sup></u> <u>Approx. 820m<sup>3</sup></u>	Secondary treatment: None Sum of the ratios to regulatory concentrations: 0.45 - 0.62 <sup>※6</sup> Tritium concentration: 220,000~380,000Bq/liter <sup>※7</sup> Total tritium volume: Approx. 1.9 T Bq	June - July
25-3-14	J1 area Group E (Transferred to Measurement/Confirmation facility group A) G5 area Group E (Transferred to Measurement/Confirmation facility group A)	<u>Approx. 7,300m<sup>3</sup></u> <u>Approx. 480m<sup>3</sup></u>	Secondary treatment: None Sum of the ratios to regulatory concentrations: 0.47 - 0.62 <sup>※6</sup> Tritium concentration: 200,000~380,000Bq/liter <sup>※7</sup> Total tritium volume: Approx. 2.9 T Bq	July - August
25-4-15	G5 area Group E/C/B (Transferred to Measurement/Confirmation facility group B)	<u>Approx. 8,970m<sup>3</sup></u> <sup>※4</sup>	Secondary treatment: None Sum of the ratios to regulatory concentrations: 0.47 - 0.62 <sup>※6</sup> Tritium concentration: 200,000~220,000Bq/liter <sup>※7</sup> Total tritium volume: Approx. 1.6 T Bq	September

Continues on next slide

※1 The management number is made up of the fiscal year, followed by the discharge number for that fiscal year, and the total number of discharges to date.

For example, "25-1-12" indicates that the data is for the first discharge of FY2025, which is the twelfth discharge to date.

※2 The tank order from which water will be transferred will not be impacted by increases/decreases in the transfer volume (factual measurements). But order of discharge may be moved forward or backward.

※3 Underlined parts are updated as actual values according to the progress of the work.

※4 Since there will be no water remaining in the receiving tanks (Measurement/Confirmation tank groups A/B) after the tank inspections, the amount of water to be transferred will total approximately 9,000m<sup>3</sup> (discharge volume is approximately 7,800m<sup>3</sup>).

※5 K3 area Group A/B tanks emptied as a result of transfer/discharge during FY2023 and FY2024 will be reused to receive ALPS treated water.

※6 Conservative values calculated from the analytical values of the seven major nuclides (Cs-134, Cs-137, Sr-90, I-129, Co-60, Sb-125, Ru-106) measured after ALPS treatment and storage in tanks, plus the maximum value of C-14 (0.11) and an estimate of the total of other nuclides at 0.3.

※7 Tank group average, estimated taking into consideration decay as of April 1, 2025.

# [Reference] FY2025 ALPS treated water discharge plan (2/2)



Continued from previous slide

Management number <sup>※1</sup>	Transfer source tank <sup>※2</sup>	Amount of water to be transferred <sup>※3</sup>	Discharge commencement period
25-5-16	G5 area Group A/B (Transferred to measurement/confirmation facility group C)	: <u>Approx. 7,780m<sup>3</sup></u> Secondary treatment: None Sum of the ratios to regulatory concentrations: 0.47 - 0.59 <sup>※4</sup> Tritium concentration: 220,000~260,000Bq/liter <sup>※5</sup> Total tritium volume: Approx. 1.9 T Bq	October - November
25-6-17	G5 area Group A/D (Transferred to measurement/confirmation facility group A) G4 north area Group A (Transferred to measurement/confirmation facility group A)	: <u>Approx. 4,050m<sup>3</sup></u> : <u>Approx. 3,710 m<sup>3</sup></u> Secondary treatment: None Sum of the ratios to regulatory concentrations: 0.46 - 0.76 <sup>※4</sup> Tritium concentration: 260,000~300,000Bq/liter <sup>※5</sup> Total tritium volume: Approx. 2.2 T Bq	November - December
Inspection suspension (including full inspections of measurement/confirmation facility Group C tanks)			
25-7-18	G4 north area Group B (Transferred to measurement/confirmation facility group B) H2 area Group J (Transferred to measurement/confirmation facility group B)	: <u>Approx. 3,760m<sup>3</sup></u> : <u>Approx. 4,040 m<sup>3</sup></u> Secondary treatment: None Sum of the ratios to regulatory concentrations: 0.58 - 0.78 <sup>※4</sup> Tritium concentration: 260,000~270,000Bq/liter <sup>※5</sup> Total tritium volume: Approx. 2.0 T Bq	March

➔ FY2025 total tritium discharge volume: Approx. 15 T Bq

※1 The management number is made up of the fiscal year, followed by the discharge number for that fiscal year, and the total number of discharges to date. For example, "25-1-12" indicates that the data is for the first discharge of 2025, which is the twelfth discharge to date.

※2 Whereas the order of the tanks from which water will be transferred will not change due to increases or decreases in the amount of water transferred (actual measurements), the discharge number may be moved up or back.

※3 Underlined parts are updated as actual values according to the progress of the work.

※4 Conservative values calculated from the analytical values of the seven major nuclides (Cs-134, Cs-137, Sr-90, I-129, Co-60, Sb-125, Ru-106) measured after ALPS treatment and storage in tanks, plus the maximum value of C-14 (0.11) and an estimate of the total of other nuclides at 0.3.

※5 Tank group average, estimated taking into consideration decay as of April 1, 2025

# [Reference] Measurement monitoring plan for obtaining quick results **TEPCO**

- Since the commencement of ALPS-treated water discharge into the sea in August 2023, TEPCO has engaged in monitoring to obtain quick measurements of the concentration of tritium in seawater at 14 locations shown in the diagrams below (Upper detection limit: Approximately 10Bq/liter). The discharge is immediately suspended if any of the values exceed the discharge suspension level (noted in the diagrams)

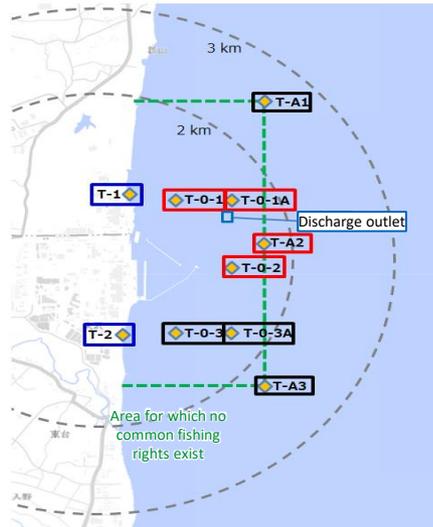


Figure 1: Specimen sampling locations within 3km of the power station (near the discharge outlet)

 
 
  : Monitoring points used to obtain quick results (10 locations)  
**Indicator (Discharge suspension level) 700Bq/liter**

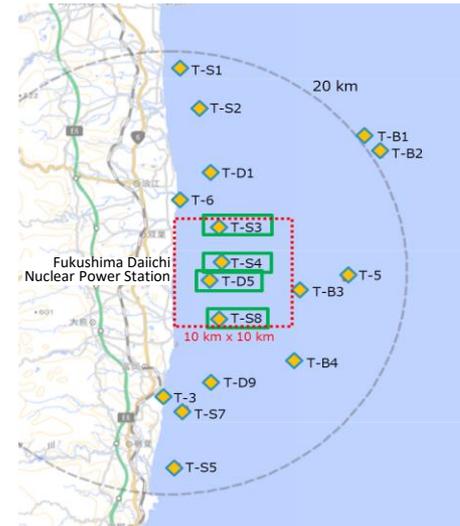


Figure 2: Specimen sampling locations within a 10km square in front of the power station

  : Monitoring points used to obtain quick results (4 locations)  
**Indicator (Discharge suspension level) 30Bq/liter**

	【Fig.1】 Within a 3km of the power station (near the discharge outlet)		【Fig. 2】 Four locations within a 10km square in front of the power station <span style="border: 1px solid green; padding: 2px;"> </span>
	Four locations in the vicinity of the discharge outlet <span style="border: 1px solid red; padding: 2px;"> </span>	Other six locations <span style="border: 1px solid blue; padding: 2px;"> </span> <span style="border: 1px solid black; padding: 2px;"> </span>	
During the discharge period and for one week after the completion of discharge	Daily <sup>※1</sup>	Twice a week <sup>※2</sup>	T-D5: Once a week T-S3, T-S4, T-S8: Once a month
During the discharge suspension period (Excluding the week following the completion of discharge)	Once a week <sup>※2</sup>	Once a month <sup>※2</sup>	

※1 If bad weather during the discharge period prevents measurements for being taken for two consecutive days, on the following day (third day) if it is again expected that measurements cannot be taken, measured results will be quickly obtained from T-1 and T-2.

※2 We have engaged in monitoring daily since the commencement of discharge in August 2023, but the monitoring plan was changed on December 26, 2023 in light of actual measurements taken during discharge ([Announced on December 25, 2023](#))
